


CUSTOM RESIDENTIAL HOUSING CONSTRUCTION: A CASE STUDY

AD-A283 822



NO0123-89-6-0549



BY

MARK W. JACKSON

A REPORT PRESENTED TO THE GRADUATE COMMITTEE
OF THE DEPARTMENT OF CIVIL ENGINEERING IN
PARTIAL FULFILLMENT OF THE REQUIREMENTS
FOR THE DEGREE OF MASTER OF ENGINEERING

This document has been approved
for public release and sale; its
distribution is unlimited.

UNIVERSITY OF FLORIDA

SUMMER 1994

94-27557



738

94 8 26 101

DTIC ORIGINATOR'S REPORT

ACKNOWLEDGEMENT

I wish to thank everyone who contributed to the development of my report. Special thanks to Mickey Smith of Mickey Smith Professional Builders INC. (MSPB), for allowing me to use his business as the basis for my report. Mr. Smith's patience and willingness to share his vast construction knowledge made this report possible. Thanks to Mr. Bill Bembry and Mrs. Diane Gebhardt of MSPB for their keen insight into Mr. Smith's daily operations. I sincerely hope that the shared experience over the past year was as beneficial to MSPB as it was to my own education and development. I would also like to thank the faculty and staff of the Civil Engineering Department at the University of Florida. Their outstanding support and genuine interest exceeded my expectations and enabled me to successfully complete graduate school. Heartfelt thanks to Ms. Sigrid Gobel, for her unwavering support and unparalleled inspiration over the past year.

Accession For	
NTIS CRA&I	<input checked="" type="checkbox"/>
DTIC TAB	<input type="checkbox"/>
Unannounced	<input type="checkbox"/>
Justification	
By <i>Form 50</i>	
Distribution /	
Availability Codes	
Dist	Avail and/or Special
<i>A-1</i>	

ABSTRACT

This report is a synopsis of research conducted with Mickey Smith Professional Builders, Inc. (a successful custom home construction firm in Gainesville, Florida). The goal was to broaden my technical engineering knowledge and gain practical construction experience.

The majority of time was spent developing a critical path construction schedule for a typical home. Although the schedule took a tremendous amount of time to develop, the results comprise only a few pages (Table 5.1 and Appendices A through D). To make the report more comprehensive, I covered the custom home construction business in general and provided insight into the steps required to build a custom home.

Certain topics were brief or left out entirely to protect proprietary knowledge inherent to Mr. Smith's operation. To address this issue, I drafted the letter found in Section 6.1.

TABLE OF CONTENTS

CHAPTER 1	1
INTRODUCTION	1
1.1 Business Background Information	1
1.2 Typical Custom Home Description	1
1.3 Custom Home Cost Breakdown	2
CHAPTER 2	4
EMPLOYEE RESPONSIBILITIES	4
2.1 Owner's Responsibilities	4
2.2 Construction Superintendent's Responsibilities	5
2.3 Administrative Assistant's Responsibilities	6
2.4 Summary	7
CHAPTER 3	8
SUBCONTRACTORS	8
3.1 Subcontract Activities	8
3.2 Subcontractor Utilization	9
3.3 Relationship between Subcontractors and Owner	9
3.4 Estimating	10
3.5 Billing Procedure	10
CHAPTER 4	11
SEQUENCE OF EVENTS	11
4.1 Customer Requests	11
4.2 Design Phase	11
4.3 Estimating Phase	11
4.4 Contract Signing	11
4.5 Construction Schedule/Change Orders	12
4.6 Occupancy	12
CHAPTER 5	13
CONSTRUCTION SCHEDULE	13
5.1 Scheduling Background	13
5.2 Construction Activity List	13
5.3 Primavera Outputs	16
CHAPTER 6	17
COMPANY FORMS	17
6.1 Initial Agreement Letter	17
6.2 Deposit Receipt and Construction Contract	18

TABLE OF CONTENTS

CHAPTER 1	1
INTRODUCTION	1
1.1 Business Background Information	1
1.2 Typical Custom Home Description	1
1.3 Custom Home Cost Breakdown	2
CHAPTER 2	4
EMPLOYEE RESPONSIBILITIES	4
2.1 Owner's Responsibilities	4
2.2 Construction Superintendent's Responsibilities	5
2.3 Administrative Assistant's Responsibilities	6
2.4 Summary	7
CHAPTER 3	8
SUBCONTRACTORS	8
3.1 Subcontract Activities	8
3.2 Subcontractor Utilization	9
3.3 Relationship between Subcontractors and Owner	9
3.4 Estimating	10
3.5 Billing Procedure	10
CHAPTER 4	11
SEQUENCE OF EVENTS	11
4.1 Customer Requests	11
4.2 Design Phase	11
4.3 Estimating Phase	11
4.4 Contract Signing	11
4.5 Construction Schedule/Change Orders	12
4.6 Occupancy	12
CHAPTER 5	13
CONSTRUCTION SCHEDULE	13
5.1 Scheduling Background	13
5.2 Construction Activity List	13
5.3 Primavera Outputs	16
CHAPTER 6	17
COMPANY FORMS	17
6.1 Initial Agreement Letter	17
6.2 Deposit Receipt and Construction Contract	18

6.3 Addendum "A" to Deposit Receipt and Construction Contract	24
6.4 Sub Quote Comparison Form	33
6.5 Customer Selections Form	36
6.6 Sample Estimate Sheet	43
6.7 Customer Material Planning Document	47
 CHAPTER 7	 51
SUMMARY AND RECOMMENDATIONS	51
7.1 Summary	51
7.2 Recommendations	51
 APPENDIX A	 53
CLASSIC SCHEDULE REPORT	53
 APPENDIX B	 56
TIME-SCALED LOGIC DIAGRAM	56
 APPENDIX C	 57
BAR CHART	57
 APPENDIX D	 58
PURE LOGIC DIAGRAM	58

CHAPTER 1 INTRODUCTION

1.1 Business Background Information

This report outlines a successful custom home construction business. The entire staff consists of three personnel (owner, construction superintendent and administrative assistant) who are capable of coordinating construction of seven houses at any one time. All design and construction work is accomplished by subcontractors. The owner and construction superintendent estimate the projects and compare their estimate to the subcontractors estimate. This comparison provides an internal check and balance against mistakes made during the estimating process and produces an accurate estimate used to evaluate subcontractor bids. Subcontractor bids are for labor only; material (procurement and delivery to the job site) is handled by the construction superintendent.

1.2 Typical Custom Home Description

Since no two custom homes are alike, I developed a list of items that were common to most of the homes being constructed:

- 3,000 square feet
- single story
- level lot
- uniform/inactive soil conditions
- negligible effects of water table on foundation design
- continuous concrete footer
- wood frame
- two-car garage
- swimming pool
- A/C and fireplace
- security system
- stereo system

The cost of a typical home runs between \$60-\$100/square foot. The large range in cost per square foot is primarily dependent upon cost of construction materials and amenities

the customer desires. Material costs vary dramatically, so a house that cost \$150,000 today might cost \$140,000 or \$160,000 tomorrow. Likewise, a home with amenities such as a sauna or Jacuzzi will cost significantly more than a home with just a shower and bathtub.

1.3 Custom Home Cost Breakdown

Refer to figure 1.1 for a breakdown of costs associated with a typical home. Notice that equipment and labor are not shown since the subcontractors incur these costs.

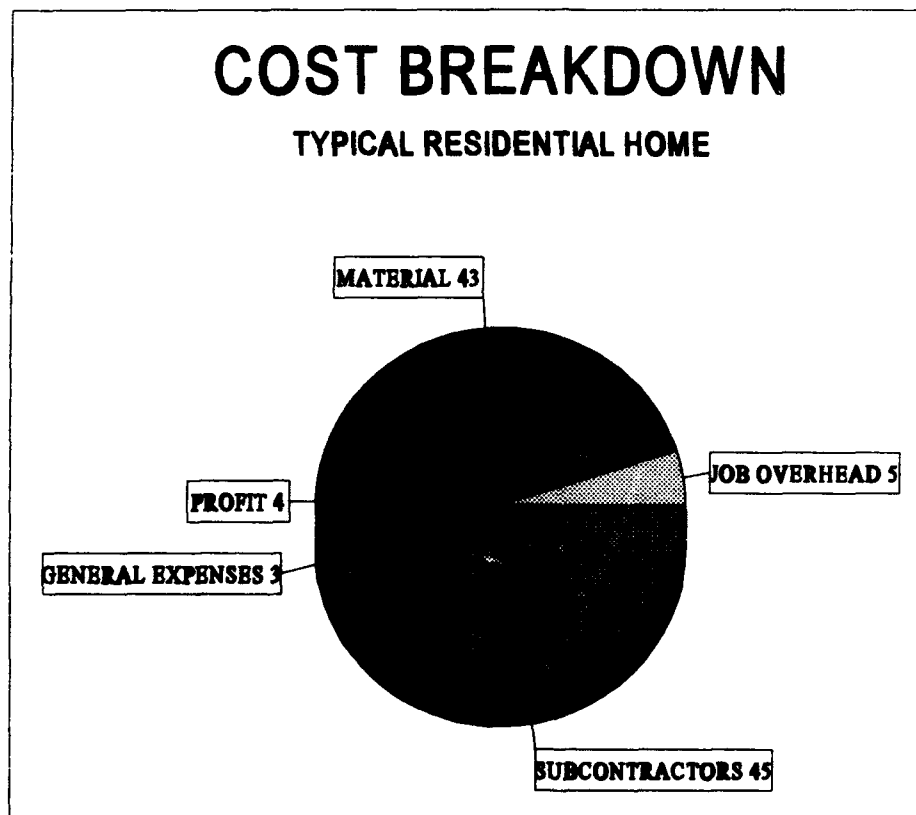


Figure 1.1 Piechart of Costs by Percentage

It is possible to survive on four percent profit, but great care must be taken when figuring general/job overhead. If these overhead figures are low, the difference comes out of the profit, leading to certain monetary losses.

CHAPTER 2

EMPLOYEE RESPONSIBILITIES

2.1 Owner's Responsibilities

The owner is a registered professional engineer, state certified residential contractor, and state registered real estate broker. In the past 12 years, he has built hundreds of homes and gained a tremendous amount of construction experience. Although he spends a good deal of time with the construction end of the operation, he believes that the most important aspect of his involvement is with financial/business matters. Specific duties include:

- acquires clients
- incurs all financial obligations
- makes financial decisions
- obtains loans if needed
- hires employees
- hires subcontractors
- negotiates/signs change orders
- ensures local, state, and federal business regulations are adhered to
- primary interface with clients
- oversees construction of all homes

The owner works constantly to ensure the success of his operation. He feels obligated to not only keep his office staff employed, but to keep his subcontractors working as well. This requires him to stay alert to housing market trends and to remain ever vigilant in his business dealings. Most of his mornings are spent touring various construction sites, resolving conflicts common to any project. Afternoons and most evenings are spent catching up on paper work and planning the next day's strategy.

2.2 Construction Superintendent's Responsibilities

A single construction superintendent oversees the construction of all houses. Specific

duties include:

- primary interface with subcontractors**
- quality control**
- project estimating**
- project scheduling**
- material ordering and scheduling**
- subcontractor quote/bid comparison**
- subcontractor selection**

The construction superintendent routinely works long hours, with his presence frequently being requested at two different locations at the same time. As several homes are constructed simultaneously, there is significant lost time due to travel. In order to reduce these instances and save travel time, a cellular phone is used. Although a great time saver, the cellular phone comes at a great price, so its use has to be controlled and justified on a continual basis.

Since only one superintendent oversees all construction, his importance to the success of the operation cannot be overemphasized. The superintendent must be knowledgeable, experienced, quick thinking, diplomatic, and energetic to effectively carry out his duties. His ability to make prudent construction and business decisions have a direct impact on the prosperity of the business. He constantly resolves discrepancies in plans/specifications and subcontractors' construction techniques. Additionally, he ensures all phases of construction are in accordance with the building code, which reduces the likelihood of future claims. Because the construction superintendent's role is so significant, extreme care must be taken when filling this position.

2.3 Administrative Assistant's Responsibilities

One administrative assistant handles all office-related duties which include:

- filing
- book keeping
- record keeping
- accounting
- payroll
- specialty material ordering/tracking
- report generation/updating

To carry out her duties, the administrative assistant uses a 486SX-25MHz computer loaded with Job Oriented Business Systems (JOBS) and Word Perfect software. JOBS is used to generate the following reports:

- accounts payable
- accounts receivable
- general ledger
- job cost
- payroll
- job scheduling

Word Perfect is the primary word processing device and is used to generate the following reports:

- deposit receipt and construction contract
- addendum "A" to contract
- sub quote comparison
- customer selections
- estimate sheet
- customer material planning document

Refer to Chapter 6 (Company Forms) for sample copies of the reports listed above.

Like the construction superintendent, the administrative assistant stays extremely busy and routinely works long hours. Aside from her regular duties, she performs additional tasks to help maintain office proficiency. She assists subcontractors in obtaining workers'

compensation, or exempt forms, and general liability insurance; compares prices from various material vendors and solicits subcontractor quotes; helps customers select/order specialty material items such as wallpaper and carpet; distributes W2's/1099's to subcontractors; generates the quarterly and annual payroll reports; and ensures subcontractors are paid on time.

2.4 Summary

Given this scenario, all three staff members are required to assist as necessary, to get the job done. It is difficult to clearly define areas of responsibility, since considerable overlapping occurs. This team-oriented working environment creates a family-type atmosphere that is conducive to the residential construction business. Everyone works toward a common goal and accepts the notion of having to do something normally required of others.

With a maximum workload each employee is critical to the process. Consequently, it is imperative that each employee be completely dedicated to the effort or the system will fail. Unlike large corporations, where the inadequacies of a few can be overcome by the rest of the organization, a business of this size has no room for sub-standard employees.

CHAPTER 3 SUBCONTRACTORS

3.1 Subcontract Activities

As previously mentioned, all design and construction is contracted out. Chapter 5, Project Planning/Scheduling, contains a comprehensive list of all construction activities performed by subcontractors. Although a typical house contains 68 construction activities, there are not 68 subcontractors. There is considerable overlapping between subs, with each handling more than one activity. For example, the foundation sub may also lay out the lot and pour all the concrete. Despite the vast amount of overlap, a typical house may still use up to 28 separate subcontractors, creating logistical challenges for the construction superintendent.

A representative subcontractor list would include:

- surveying
- soil analysis
- concrete, driveway, and walk
- plumbing
- HVAC and gas lines
- electric
- framing
- trusses
- roofing
- security system
- stereo
- insulation
- aluminum soffit
- acrocrete and drywall
- masonry
- spa
- swimming pool
- windows, mirrors and shower doors
- door hardware, garage door and vinyl shelving
- doors
- ceramic tile

- cabinets
- carpet and wallpaper
- wallpaper installation
- trim carpentry
- paint
- landscape
- house cleaning

3.2 Subcontractor Utilization

With 28 subs per house and 7 houses being built at once, coordination between the parties is quite difficult. To mitigate this problem, efforts are made to use the same subs on all houses. This practice greatly reduces confusion and delays since the owner and subcontractor deal with each other on a regular basis. Since each knows what is expected of the other (quality and timeliness of work), delays due to familiarization time, scheduling conflicts, or improper work methods/procedures are reduced.

3.3 Relationship between Subcontractors and Owner

The construction superintendent (CS) is the primary interface between the owner and the subcontractors (the owner in this instance is Mickey Smith Professional Builders vice the homeowner). The CS compares price quotes/bids from the subs, chooses the best sub for the job, schedules the subs, and monitors their performance throughout the construction process. Due to the CS's considerable experience, he handles most design/constructability issues directly at the job site with the subcontractor foreman. The CS then discusses these issues with the owner, who will then resolve the issues with the homeowner. At this point, the owner and homeowner decide on alternative solutions and their related cost.

3.4 Estimating

The estimating process can become complicated for three reasons: the large number of subcontractors involved, the subs estimating for labor only (the owner handles material and equipment), and the necessity to keep the plans/specifications in the office (to prevent unauthorized dissemination of the plans). Once all prospective subs have bid the job, the CS compares the bids and chooses a suitable contractor.

3.5 Billing Procedure

The billing procedure follows a three step process: Step 1 - Subcontractors submit their bills for all work-in-place by Wednesday of each week; Step 2 - The construction superintendent verifies all work-in-place with the administrative assistant; Step 3 - The administrative assistant pays all subs for verified work-in-place.

CHAPTER 4

SEQUENCE OF EVENTS

There are seven basic steps involved in the business of residential home construction:

- customer request
- design
- estimate
- contractual agreement
- construction schedule executed
- payment
- occupancy

4.1 Customer Requests

The number of customer requests is primarily dependent on the current housing market. Additionally, the business receives many prospective homeowners through referrals from previous clients.

4.2 Design Phase

Some clients have pre-engineered designs and only need help during the construction phase. Others develop design criteria by examining completed houses and making necessary changes to suit their needs. There are also those clients who have no design ideas and require plans to be developed from scratch.

4.3 Estimating Phase

Once the design is complete, an estimate is generated. As previously stated, the various subcontractors provide labor estimates while MSPB provides material and equipment estimates. Refer to Section 6.6 for a sample estimate sheet.

4.4 Contract Signing

Once the estimate is complete, the construction contract is signed (refer to Section 6.2 for a sample construction contract). The contract establishes a six stage payment schedule that can be summarized as follows:

- 1st stage: footings, slab, and underslab utilities completed
- 2nd stage: structure dried-in; includes trusses, sheathing, felt, and interior partitions
- 3rd stage: rough plumbing/electrical, A/C duct work, and security pre-wire completed
- 4th stage: roof, exterior wall sheathing, window installation, insulation, and interior walls completed except for paint and trim carpentry
- 5th stage: cabinets, interior doors, wall base, and ceramic tile installed
- 6th stage: construction/clean-up complete and issuance of Certificate of Occupancy

The contract further specifies that disputes be resolved through arbitration and the homeowner may not interfere with construction at the job site.

4.5 Construction Schedule/Change Orders

Although Chapter 5 addresses the construction schedule in detail, it is important to note how changes are negotiated. Any change must be agreed upon by both the homeowner and MSPB with the cost associated with the change reflected in the amount due at the next construction progress payment. Additionally, all changes must be in writing and signed by both parties, except for allowance changes, which may be increased or decreased without change orders. Verbal change orders, agreed to by both parties, shall be paid for by the homeowner within seven days after completion of the added work.

4.6 Occupancy

Once all construction improvements are complete and payment is received, a Certificate of Occupancy is issued which completes the process.

CHAPTER 5

CONSTRUCTION SCHEDULE

5.1 Scheduling Background

Prior to my involvement with MSPB, no formal project planning/scheduling was performed. Since the owner and construction superintendent are extremely knowledgeable and have years of construction experience, most planning and scheduling comes naturally. As the steps required to build residential houses are repetitive and rarely change, there is no need for sophisticated computer driven scheduling software.

I did, however, expose the owner to two scheduling software programs: CPM 18 and Primavera. After reviewing the outputs, cost, and user-friendliness of both software packages, the owner chose to use CPM 18 for his project scheduling.

Since Primavera is more versatile than CPM 18, I will use Primavera to provide a comprehensive look at a typical house construction schedule.

5.2 Construction Activity List

Table 5.1 is an activity list that was generated by myself and the owner. I visited numerous project sites to develop accurate construction activities, durations, and dependencies. Where durations were not directly observed, the owner and construction superintendent provided the missing information. Likewise, when questions on dependencies arose, answers were provided by the owner and construction superintendent. We considered the use of advanced dependencies, which would provide a more accurate schedule, but declined to use them because finish to start relationships were sufficient to suit the owner's needs.

Table 5.1 - Construction Activity Listing

ACTIVITY #	DESCRIPTION	DURATION	DEPENDS ON
1	OBTAIN BUILDING PERMIT	7	----
2	WATER METER	7	----
3	SURVEY	1	1
4	ORDER TRUSSES/WINDOWS	20	1
5	CLEAR/GRUB	2	3
6	STAKED OUT	1	5
7	POUR FOOTING	3	2,6
8	FOUNDATION BLOCK	2	7
9	SLAB FILL	1	8
10	SLAB PLUMBING/DRYER VENT	1	9
11	A/C CONDENSER LINES	1	10
12	SLAB ELECTRIC/JENN AIRE VENT	1	10
13	SOIL POISON	1	11,12
14	SLAB INSPECTION	1	13
15	POUR SLAB	2	14
16	WOODEN DECK	2	15
17	EXTERIOR WALLS	2	15
18	INTERIOR WALLS	2	17
19	SET TRUSSES	1	4,17
20	HANG EXTERIOR SHEATHING	2	17
21	FASCIA	1	19
22	STUCCO	4	20
23	BRICK/STONE	15	20
24	DRY-IN	4	21
25	PLUMBING STACK-OUT	2	18,24
26	A/C DUCT WORK	4	24
27	FIXED GLASS	1	24

Table 5.1 - continued

28	SET WINDOWS	1	24
29	ROUGH ELECTRICAL	6	24
30	SIDING	3	28
31	SECURITY PRE-WIRE	1	29
32	STEREO/TV/INTERCOM PRE-WIRE	1	29
33	ROOFING	3	29
34	SOFFIT	3	22,23,30
35	EXTERIOR PAINT	3	22,30
36	SECURITY TRIM	1	27,31
37	STEREO/TV/INTERCOM TRIM	1	32
38	FRAMING INSPECTION	1	25,26,33
39	PORCH SCREENING	2	35
40	INSULATION	2	38
41	HANG GYP-BOARD	7	40
42	HARDCOTE	4	41
43	FINISH CARPENTRY	4	42
44	SWIMMING POOL	25	42
45	GARAGE DOOR	1	42
46	CERAMIC TILE/WINDOW SILL	7	42
47	MEDICINE CABINET	1	43
48	PAINT INTERIOR	6	43
49	SET ELECTRICAL PANEL/LOCK HOUSE	1	43
50	SITE CLEANUP	2	16,39,44
51	FIRE-PLACE VENEER	1	48
52	CABINETS/VANITIES	5	48
53	SEMI-PERM ELECTRIC	2	45,49
54	FINAL GRADE	2	50
55	APPLIANCES	1	52

Table 5.1 - continued

56	WALLPAPER	5	52
57	A/C PADS	1	54
58	DRIVEWAY/SIDEWALK	3	54
59	PLUMBING TRIM	3	55
60	MIRRORS	1	56
61	HVAC TRIM	3	57
62	CARPET/VINYL FLOORING	3	58
63	LANDSCAPE	8	58
64	ELECTRICAL TRIM	5	53,57,59
65	SHOWER DOORS	1	60
66	WOOD FLOORING	8	61
67	HOUSE CLEANUP	3	34,46,47,51,62,64,65, 66
68	FINAL INSPECTION	1	36,37,63,67

5.3 Primavera Outputs

Refer to Appendices A through D to review the following construction schedule

outputs:

- classic schedule report
- time-scaled logic diagram
- bar chart
- pure-logic diagram

**CHAPTER 6
COMPANY FORMS**

6.1 Initial Agreement Letter

2600 SW Williston Road
Apartment #708
Gainesville, FL 32608
October 8, 1993

Mr. Mickey Smith
Professional Builders Inc.
2831 N.W. 41st Street
Suite G
Gainesville, FL 32606

Dear Mr. Smith:

This letter pertains to our conversation of 8 October in which we discussed my Thesis related work with your company.

As research for my Thesis on contractor operations, I will familiarize myself with the functions of your organization. I understand that I will receive no monetary compensation for any service I may provide. Additionally, you will not be liable for any injuries I may incur during this process nor will I be liable for unintentional mistakes. I will document my research in the form of a technical report that will be used solely to satisfy my degree requirements. You maintain the right to review the report before its submission to insure only appropriate information is divulged.

Sincerely,

Mark W. Jackson
LT, CEC, USN

6.2 Deposit Receipt and Construction Contract

DEPOSIT RECEIPT AND CONSTRUCTION CONTRACT

DATE: _____

RECEIPT IS HEREBY ACKNOWLEDGED by _____, a
Florida corporation, hereinafter called "Contractor", whose address is _____
_____, of _____ DOLLARS (\$ _____ .00)
from _____ and _____

Address: _____
Telephone: (____) ____ - _____, hereinafter called "Owner", as a guarantee for construction
expenses on the following described improvements which contractor agrees to construct,
erect and finish upon the following described real property in _____ County,
Florida, and for which Owner agrees to pay or cause to be paid unto the Contractor upon
the terms and conditions hereinafter set forth:

**1. LEGAL DESCRIPTION OF REAL ESTATE LOCATED IN _____
COUNTY, FLORIDA:**

Lot _____ (____), _____, a subdivision as per plat
thereof recorded in Plat Book "____", Page _____ of the Public Records of
_____ County, Florida.

2. DESCRIPTION OF IMPROVEMENTS:

A single family residence constructed in accordance with plans _____
_____ with a date of _____
said plans and specifications forming a part of this contract as fully as if attached
hereto or repeated herein. Addendum "A", containing allowances for certain
included items covered by this contract, is attached hereto and made a part
hereof. It is agreed that the constructed residence may, because of unforeseen
occurrences deviate from the plans and specifications.

3. TERMS OF PAYMENT:

Owner agrees to pay and contractor agrees to accept the total contract price of
_____ (\$ _____ .00) in progress payments as
follows:

- (a) The sum of \$ _____ as a binder deposit, by check subject to collection receipt of which is hereby acknowledged.

All payments will be in accordance with the construction lenders draw schedule or:

- (b) The sum of \$ _____ upon the completion of the First stage of construction.
- (c) The sum of \$ _____ upon the completion of the Second stage of construction.
- (d) The sum of \$ _____ upon the completion of the Third stage of construction.
- (e) The sum of \$ _____ upon the completion of the Fourth stage of construction.
- (f) The sum of \$ _____ upon the completion of the Fifth stage of construction.
- (g) The sum of \$ _____ plus any additional charges for changes agreed upon between Owner and Contractor upon the acceptable completion of the SIXTH stage of construction.

The Six (6) stages of construction for the purposes of progress payments provided herein shall be defined as follows:

FIRST: When the slab is complete with footings, foundation walls, rough-in plumbing, condensate lines, and under slab electric.

SECOND: Structure is dried-in, including trusses, roof sheathing, felt and interior partitions.

THIRD: (a) Plumber has run stacks through the roof and extended the lines up from the slab.

(b) Electrician has finished the rough wiring.

(c) Air conditioning subcontractor has installed the duct work.

(d) Security system, if included, is pre-wired.

FOURTH: When the roof is complete, the exterior walls are sheathed, the windows are installed, and insulation and interior walls are finished except for paint and trim carpentry.

FIFTH: Cabinets, interior doors, and wall base are installed; and ceramic tile walls are complete.

SIXTH: Completion of construction including clean-up, and issuance of a Certificate of Occupancy by _____.

As used with this contract, the term "acceptable" shall mean upon the approval of the _____ building inspector.

Disbursement shall be made by owner within five (5) days notice of said completion of each stage. Contractor shall execute a payment affidavit that Contractor's employees, suppliers and subcontractors have been fully paid for all work completed to the date of said disbursements.

In the event that the Owner fails to disburse any progress payment within five (5) days of notification from the Contractor that same is due, Contractor shall have the option of charging interest on the amount due at the highest rate permitted by law or pursuing any and all other remedies provided by law.

3.1 It is agreed that Owner may not withhold payment of all or a portion of the amount due because of any disagreement between Contractor and Owner relating to quality, design, or cost of any of the construction. All adjustments, if any, shall be made at the time of closing as established below.

3.2 Before closing, a list shall be agreed upon by the Owner and the Contractor of any items which are incomplete or otherwise unsatisfactory, which items shall be corrected or finished by Contractor within sixty (60) days after closing, weather and material availability permitting. As to such items, the owner shall be entitled to any remedy provided by law or in equity for the Contractor's failure to complete or correct such items.

3.3 Defects, if any, first appearing after closing shall be handled (a) in accordance with the provisions of the Home Owners Warranty Corporation Insurance/Warranty Documents, or, in the event of a dispute which does not involve a matter of warranty, (b) by compulsory arbitration pursuant to this contract.

3.4 Subject to paragraph 3.3 above, closing of the purchase by the Owner shall constitute acceptance by Owner of the structure as built and Owner's acknowledgment that the structure has been constructed or completed in accordance with the contract documents and Contractor has complied with his obligations. If requested by

Contractor, Owner shall execute a "Letter of Acceptance" in a form satisfactory to the Contractor, certifying that the improvements are and have been completed in substantial conformity with the requirements of this contract.

3.5 Possession of the structure shall be given to the Owner at closing and in no event shall Owner occupy the structure nor allow any person to occupy same until construction has been completed and payment is made in full of the contract sum and any authorized additions thereto, provided Contractor is not in default of the terms hereof.

4. CONSTRUCTION:

(a) This agreement is contingent upon Owner obtaining a construction loan in the amount of _____ within 30 days of full execution of this agreement. Owner shall use their best effort to obtain such a loan. In the event said financing is not obtained by Owner within said period, Contractor shall be entitled to keep the deposit made this day as liquidated damages for its design work and this contract and the Contract For Sale and Purchase also signed this date thereupon be cancelled and all further obligations from one party to the other shall be null and void.

(b) Contractor agrees to construct a house upon the above described lot in accordance with paragraph 2 herein, the plans and specifications of which are hereby approved by the Owner and are on file in the contractor's office.

(c) Construction of the house by Contractor shall be completed within _____ from the date of beginning construction, subject to weather, availability of materials and change orders requested by the owner.

(d) Any additions to or deletions from the improvements described in paragraph 2 shall be agreed upon between the Contractor and Owner. The additional cost or deduction will be reflected in the amount due at the next construction progress payment. All changes should be reduced to writing and signed by the parties hereto, with the exception of allowance changes which may be increased or decreased without change orders. Changes verbally agreed to by Owner and Contractor that because of time or schedule constraints are not reduced to writing immediately shall be paid for by the Owner within seven (7) days after the completion of the added work.

5. The Contractor shall perform all work in good and workmanlike manner in substantial accordance with plans and specifications. Should any dispute arise regarding the construction; or the meaning of the drawings or specifications; or respecting the true value of any extra work; or of work omitted; the dispute shall be evaluated and decided by

two competent persons -- one employed by the Owner and the other by the Contractor -- and those two shall have the power to name an arbitrator, whose decision shall be binding on all parties.

6. Owner agrees not to interfere with the construction on the premises during working hours, and to present any questions and discuss all matters pertaining to construction at the office of the Contractor. Owners, their guests and family enter on the site at their own risk and agree to hold the contractor harmless for any injuries or damages at the site.

7. The Contractor, at its own cost, is to provide all manner of materials and labor for the due performance of the work unless specifically excepted below:

EXCEPTION: Site conditions differing in excess of ten percent of the cost included in this contract (\$_____) will be added by change order to the costs of the Owner. Site conditions include elevation changes, soil conditions, ground water, drainage, off-site unanticipated problems etc.

8. The Owner shall not be accountable for any loss or damage that shall or may happen to the said work, or any part or parts thereof, or for any of the materials or other things used and employed in finishing and completing the said improvements until completion of all improvements, unless the owner provided said parts or materials.

9. The Contractor will continually insure the improvements for their full value, and the policy will not expire until after the acceptable completion of the improvements.

10. The Contractor will make oath according to the laws of the State of Florida, that each artisan, laborer and materialman has been paid in full, and that there are no unpaid accounts against the improvements called for hereunder upon completion of each stage of construction prior to payment by owner.

11. All notices from one party to the other shall be hand delivered or mailed to the party at the respective addresses given above. Notices shall be deemed given on the date of receipt by the party for whom notice is intended.

12. This contract embodies the entire agreement and understanding of the parties hereto and may not be changed, altered or modified except by an instrument in writing, signed by the Owner and the Contractor.

13. It is intended that disputes be resolved per arbitration in accordance with paragraph (5), however, if any litigation arises under this agreement between Owner and Contractor, the prevailing party shall be entitled to recover from the nonprevailing party all reasonable costs incurred in the trial court and on appeal by the prevailing party including a reasonable attorney's fee.

14. Contractor shall provide, at no additional cost to the Owner, the standard ten (10) year Home Owner's Warranty Corporation protection policy. The provisions of this policy govern the warranty on this residence. Materials, equipment and Subcontractor work supplied by the Owner will not be covered by the Contractor's warranty, and will be the responsibility of the Owner. Swimming pool, and related screen enclosure, if any, along with landscaping and irrigation will be warranted by the appropriate Subcontractor and not the Contractor.

15. RADON GAS: Radon is a naturally occurring radioactive gas that, when it has accumulated in a building in sufficient quantities may present health risks to persons who are exposed to it over time. Levels of Radon that exceed federal and state guidelines have been found in buildings in Florida. Additional information regarding Radon and Radon testing may be obtained from your county public health unit.

16. Both parties agree that the project will begin, progress and end in the spirit of mutual cooperation and fairness in all matters.

IN WITNESS WHEREOF, the said parties to this contract have hereunto affixed their signatures.

CONTRACTOR:

By: _____ Date: _____

OWNER:

_____ Date: _____

_____ Date: _____

6.3 Addendum "A" to Deposit Receipt and Construction Contract

ADDENDUM "A" to CONTRACT DATED _____

BUILDING CONCRETE:

Foundation footings of _____ psi concrete reinforced with _____ # _____ reinforced steel bars.

_____ inch concrete slab reinforced with _____ steel wire mesh.

Six mil visqueen moisture barrier under living area and garage.

Soil poisoned area beneath building. Application will be at rate per pest control company's specifications at expansion joints, perimeter walls, and foundation walls. Pest Control Company will furnish owner with a written guarantee with a damage replacement clause. Owner will be required to comply with annual treatments after first year.

EXTERIOR:

MASONRY:

Foundation block per plans.

Stone Allowance: _____, Brick Allowance: _____

Mortar Allowance: _____

CARPENTRY:

Framing lumber for walls to be 2x4 Spruce, SPF or equivalent spaced _____ on centers for bearing walls.

Roof sheathing to be _____ " thick with plyclips, covered with 15# felt.

Fascia _____, Soffits _____

Pressure treated lumber will be used in areas where lumber is in contact with concrete or masonry.

Load bearing trusses to be designed by licensed structural engineer with hurricane clips on all trusses.

STAIRS:

Interior stair allowance for handrail, brackets, newel posts balusters, stair treads, etc., erection labor and painting _____ or staining _____ allowance _____

Rough carpentry for stair structure is included in carpentry.

Carpeting, if any, is included under carpet allowance.

INTERIOR TRIM:

Upstairs base type _____, Size _____, Painted _____, Stained _____

Down stairs base type _____, Size _____, Painted _____, Stained _____

Shoe Mold: _____

Closet Shelving Allowance: _____

Book Shelves: _____

Built Ins: _____

Crown Mold: _____

Window Sills: Marble _____, Wood _____

Chair Rail: _____

INSULATION:

Exterior wall insulation for living area walls: _____

Radiant barrier: _____

Ceiling insulation for all living spaces: _____

Sound insulation: _____

Wall sheathing: _____

Interior walls: _____

Resilient Channel: _____

ROOFING:

Roofing shall be: _____
Limited manufacturer's warranty: _____
Roof ventilation: _____
Gutter Allowance: _____ Skylights per plans: _____

DOORS:

Exterior doors to be wood solid core 1 3/4". Interior doors to be _____
1 3/8" thick. Interior door facing trim: _____
Metal clad doors: _____
Front door allowance: _____
Interior doors: _____
Bifold doors: _____
Door casing and jambs: _____; painted
_____, stained: _____
Sliding glass doors: _____
Door hardware allowance _____ for all exterior and interior doors.

**STANDARD ANTIQUE BRASS HINGES ARE INCLUDED ON ALL DOORS.
CHROME OR BRASS HINGES ARE AN EXTRA COST WHICH WILL BE
CHARGED TO OWNER'S DOOR HARDWARE ALLOWANCE.**

WINDOWS:

Aluminum: _____, Wood: _____, Screens: _____
Color of frames _____, Insulated: _____
Tinted Glass: _____
Hardcote returns: _____
Wood jambs and casings: _____

GLASS:

Fixed Glass: _____
Mirrors-Full width over bathroom vanities: + - 42" high.
Other Mirrors: _____

INTERIOR FINISHES:

Walls: _____
Ceilings: _____
Corner Bead: _____
Wallpaper Allowance: _____ labor and materials
Wallpaper locations: _____

PAINING:

Exterior: _____
Exterior Trim: _____
Interior Walls and Ceilings: _____

One color for the interior is included in the cost of this contract. Additional color(s) will be at additional cost.
Doors: _____
Interior Wood Trim: _____

CERAMIC TILE, GLASS BLOCK AND BATH ACCESSORIES:

Allowance for all ceramic tile, bath accessories, and window sills: _____ for labor and materials.
All walls are mud set.
Glass block allowance: _____ labor and materials

FLOORING:

Wood Flooring Allowance: _____ labor and materials
Wood Floor Type: _____
Areas of wood flooring: _____
Resilient Flooring Allowance: _____ labor and materials
Areas of resilient flooring: _____

Carpet and padding allowance: _____ labor and materials
Areas of carpeting: _____

APPLIANCES:

Allowance for purchase, shipping, and installation _____
range/cooktop: _____, refrigerator: _____
freezer: _____, oven: _____, dishwasher: _____
disposer: _____, instant hot: _____, washer: _____
dryer: _____, compactor: _____, microwave: _____
Owner supplying the following: _____

FIREPLACE:

Allowance: _____, Type: _____
Mantle: _____, Facing: _____
Hearth: _____, Height: _____
Glass doors are included; fireplace fans are not included.

GARAGE:

Garage door and opener allowance: _____ labor and materials
Ceilings: _____, Walls: _____
Other: _____

WOODEN DECKS:

FENCES:

SECURITY SYSTEM:

Key Pads: _____, Location: _____
Smoke alarms per local governing code.

CABLE TV:

Number of prewired outlets included: _____

TELEPHONE OUTLETS:

Number of prewired outlets included: _____

STEREO WIRING:
_____**CABINETS:**

Total Allowance: _____

Kitchen and baths (cabinets and counters): _____

Counter Tops Specifications: _____

Laundry Room: _____

Other cabinets: _____

ELECTRICAL:

All electrical wiring will be per plans and shall meet or exceed the appropriate local Electric Code. Additional switches, receptacles, etc., added or deleted will be added to or credited on a change order.

_____ amp service with circuit panel.

_____ Exterior 110 volt weather proof outlets.

_____ Heavy duty 220 volt outlets for power tools, etc., additional costs per circuit.

Lighting Fixture Allowance: _____ including interior and exterior lights and bulbs, dimmers.

Ceiling Fan Allowance: _____

Prewire for pool and pool light: _____

Prewire for _____ ceiling fans.

Light switch covers and receptacle covers: _____

Smoke detectors are included in security system, and will be placed in accordance with local code requirements.

HEATING AND AIR CONDITIONING:

Heat pumps: _____, Gas Furnaces: _____, Electric A/C: _____

Zones: _____

Electronic Air Cleaners: _____, Heat Recovery: _____

Duct System to be 1" rigid fiberglass ductboard, stapled and taped with foil tape.

Supply runouts to be flexible. Registers to be aluminum curved blade with damper.
Air supply registers for walk-in closets included.

PLUMBING:

Color of Fixtures: _____
Tubs: _____, Trim: _____
Spa Allowance: _____, Trim: _____
Lavatories: _____, Trim: _____
Water Closets: _____
Kitchen Sink: _____, Trim: _____
Laundry Sink: _____, Trim: _____
Plumbing Specialties: _____

Washer and Dryer connections included. Dryer vent to exterior included.

Water Heaters: _____
Hot water recirculating lines: _____
Copper interior water lines. PVC waste lines. Water supply to house shall be PVC.
Floor drain in utility room: _____
Ice maker hook up in kitchen: _____
Hose bibbs included: _____
Gas lines connections: _____

LANDSCAPING:

Allowance for lawns, plantings, irrigation system, final grade, mulch, topsoil, and etc.,
_____ labor and materials. Top soil required for grading will be charged
against this allowance. Owner acknowledges that all landscaping and irrigation will be
warranted by selected subcontractor and Mickey Smith Professional Builders, Inc. will
have no responsibility or liability for warranty. Existing trees and foliage cannot be
warranted against demise or damage. Owner's request for safeguarding existing
trees/foliage will be honored to the best of the Contractor's abilities.

EXTERIOR CONCRETE:

Driveway and walks allowance: _____
Front stoop, standard finish broom swept concrete.
Front stoop allowance: _____
Lanai/Patio allowance: _____
Planter allowance: _____

SWIMMING POOL AND ENCLOSURE, IF APPLICABLE:

Allowance: _____, Size: _____
Deck: _____, Equipment: _____
Light: _____, Diving Board: _____
Screen Enclosure: _____

Owner acknowledges that pool, deck, and screen enclosure work will be by the selected subcontractor and that Mickey Smith Professional Builders, Inc. will have no responsibility or liability for warranty.

WARRANTY: H.O.W. TEN YEAR PROTECTION POLICY.
WARRANTY COVERAGE AND PERFORMANCE STANDARDS PER HOW
FORM 500 111, REV 991.

SPECIALTIES:

Safe: _____
Attic Ladder: _____
Medicine Cabinets Allowance: _____
Vacuum System: _____
Shower Door Allowance: _____
Mailbox Allowance: _____
Grab Bars Allowance: _____
Skylights Allowance: _____
Wet Bar Allowance: _____
Bar-B-Que Allowance: _____
Well Allowance: _____
Septic Tank Allowance: _____
Shutters Allowance: _____
Ironing Board: _____
Other: _____

SPECIAL CONSTRUCTION:

Delivery and taxes paid on any allowance materials are charged against owner's allocated allowance.

**ANYTHING NOT SPECIFICALLY INCLUDED IN EITHER THIS CONTRACT
OR THE SUBJECT PLANS IS SPECIFICALLY EXCLUDED.**

6.4 Sub Quote Comparison Form

SUB QUOTE COMPARISON

FOR BIDS ON JOB: _____

DATE: _____

JOB/SUB	SIZE/QUANTITY	BID AMOUNT
A/C		
TEACO	_____	_____
BOUNDS	_____	_____
MID FL	_____	_____
BERTIE	_____	_____
CABINETS		
MAYO	_____	_____
FIELDS	_____	_____
BUSBY	_____	_____
ACCENT CABINTRY	_____	_____
CERAMIC TILE		
TAYLOR	_____	_____
CONTEMP TILE	_____	_____
DOOR HARDWARE		
DYNA-FIT	_____	_____
GATOR DOOR	_____	_____
MANNING	_____	_____
ELECTRICAL		
BILSKY	_____	_____

FRAMING

THOMAS

GARAGE DOOR

DYNA-FIT

LESTER

INSULATION

KAPLAN-STEIN

SUNCOAST

MIRRORS

GOLDEN GLASS

PLASTERING

MAX DANFORD

HENRY PENNY

SOUTHERN

PLUMBING

BILLY JOHNSON

SHELVING

DYNA-FIT

SHOWER DOORS

GOLDEN GLASS

TRIM

GATOR DOOR

MANNING

WHITTEMORE-LABOR

TRUSSES

RIDGEWAY

I&R

WINDOWS

1ST CLASS

WINDOW MAKER

PAN AM

GOLDEN GLASS

6.5 Customer Selections Form

CUSTOMER SELECTIONS

NAME _____

ADDRESS _____

PHONE # HOME- _____

LOT # _____

PHONE # WORK- _____

LOCATION: _____

DECORATOR:

PHONE # _____

ARCHITECT: _____

EXTERIOR:

BRICK: _____

WINDOWS: _____

MORTAR: _____

EXTERIOR WINDOW TRIM: _____

SHUTTERS: _____

SHINGLES: _____

SIDING: _____

SIZE: _____

PAINT COLOR: _____

BUTT: OR MITRED CORNERS: _____

TRIM: _____

WINDOW SILLS: _____

ROOF METAL: _____

GUTTERS: _____

DOORS: _____

DOOR COLOR: _____

FASCIA: _____

SOFFIT: _____

GARAGE DOOR: _____

NO. TRANSMITTERS: _____

FIREPLACE:

HEARTH: _____

MANTLE: _____

TILE: _____

GROUT: _____

CERAMIC TILE:

SUPPLIER: _____

GROUT: _____

POWDER ROOM: _____

GROUT: _____

MASTER BATH: _____

GROUT: _____

KITCHEN: _____

GROUT: _____

BATH #1: _____

GROUT: _____

BATH #2: _____

GROUT: _____

BATH #3: _____

GROUT: _____

BATH #4: _____

GROUT: _____

FOYER:

FLOORING: _____
PAINT COLOR: _____

WALLPAPER: _____
LIGHTING: _____

INTERIOR FINISHES:

DRYWALL: _____
CEILING TEXTURE: _____

HARDCOAT: _____

INTERIOR TRIM:

SUPPLIER: _____
PAINTED: _____

STAINED: _____
ROOMS: _____

INTERIOR DOORS:

SUPPLIER: _____
PAINTED: _____
HARDWARE: _____
E/D HARDWARE: _____
E/D PAINTED: _____

STAINED: _____
HINGE COLOR: _____
FRONT DOOR: _____
E/D STAINED: _____
OTHER: _____

CABINETS:

CABINET MAKER: _____

KITCHEN: _____

VANITIES:

POWDER ROOM: _____
MASTER BATH: _____
BATH #2: _____
BATH #4: _____

BATH #3: _____

CLOSET SHELVING:

WOOD: _____

CLOSET MAID: _____

WALLPAPER:**SUPPLIER:** _____**LIVING ROOM:** _____**DINING ROOM:** _____**MASTER BEDROOM:** _____**BEDROOM #2:** _____**BEDROOM #3:** _____**BEDROOM #4:** _____**LAUNDRY ROOM:** _____**POWDER ROOM:** _____**KITCHEN:** _____**BREAKFAST ROOM:** _____**OTHER ROOMS:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**BORDER:** _____**SECURITY:****INTERCOM:** _____**STEREO:** _____**ELECTRICIAN:****LIGHTING:** _____**SUPPLIER:** _____**FRONT DOOR:** _____**OTHER EXTERIOR DOORS:****GARAGE DOORS:** _____**GARAGE INTERIOR:** _____**CLOSETS:** _____**HALLWAYS:** _____**UTILITY ROOM:** _____**LIGHTING GRIDS:** _____**BATHROOM LIGHTING:****MASTER BATH:** _____**BATH #2:** _____**BATH #3:** _____**BATH #4:** _____**POWDER ROOM:** _____

BEDROOM LIGHTING:

MASTER BEDROOM: _____
BEDROOM #3: _____
KITCHEN: _____
DINING ROOM: _____
FAMILY ROOM: _____

BEDROOM #2: _____
BEDROOM #4: _____
BREAKFAST ROOM: _____
LIVING ROOM: _____

FANS:

SUPPLIER: _____
BEDROOM #2: _____
BEDROOM #4: _____

MASTER BEDROOM: _____
BEDROOM #3: _____
OTHER: _____

APPLIANCES:

COLOR: _____
MICROWAVE: _____
TRIM KIT: _____
HOOD: _____
DISHWASHER: _____
REFRIGERATOR: _____
COMPACTOR: _____
WASHER: _____

SUPPLIER: _____
RANGE: _____
OVEN: _____
TRIM KIT: _____
DISPOSER: _____
TRIM KIT: _____
HOT WATER DISPENSER: _____
DRYER: _____

OTHER ITEMS:

LAUNDRY TUB: _____
OTHER: _____

IRONING BOARD: _____

MEDICINE CABINETS:

MASTER BATH: _____
BATH #3: _____

BATH #2: _____
BATH #4: _____

SPECIALTIES:

STAIRS:

HANDRAIL: _____

HANDRAIL BRACKETS: _____

ADDITIONAL INFORMATION: _____

PLUMBING:

SUPPLIER: _____

KITCHEN: _____

WET BAR: _____

POWDER ROOM: _____

LAVATORY: _____

WATER CLOSET: _____

COLOR: _____

FAUCET: _____

ACCESSORIES: _____

MASTER BATH:

SPA: _____

SPA FACET: _____

LAVATORY FACET: _____

ACCESSORIES: _____

FIXTURE: _____

COLOR: _____

LAVATORY: _____

WATER CLOSET: _____

BIDET: _____

SHOWER OR TUB ENCLOSURE: _____

BATH #2:

COLOR: _____

FAUCET: _____

ACCESSORIES: _____

SHOWER OR TUB ENCLOSURE: _____

LAVATORY: _____

WATER CLOSET: _____

BATH #3:

COLOR: _____

FAUCET: _____

ACCESSORIES: _____

SHOWER OR TUB ENCLOSURES: _____

LAVATORY: _____

WATER CLOSET: _____

BATH #4:

COLOR: _____

FAUCET: _____

ACCESSORIES: _____

SHOWER OR TUB ENCLOSURES: _____

LAVATORY: _____

WATER CLOSET: _____

MIRRORS:

BATH ROOM ACCESSORIES, TOWEL BARS, ETC:

WOOD FLOORING:

SUPPLIER: _____
LIVING ROOM: _____
OTHER: _____

FOYER: _____
FAMILY ROOM: _____

VINYL:

LAUNDRY ROOM: _____
OTHER: _____

BREAKFAST ROOM: _____

CARPET:

SUPPLIER: _____
LIVING ROOM: _____
DINING ROOM: _____
FAMILY ROOM: _____
MASTER BEDROOM: _____
MASTER BATH: _____
BEDROOM #2: _____
BEDROOM #3: _____
BEDROOM #4: _____
POWDER ROOM: _____

STUDY: _____
BATH: _____
BATH: _____
BATH: _____

BUILT-INS:

DESK: _____
BOOKCASES: _____
OTHER: _____

OUTSIDE ITEMS:

POOL CONTRACTOR: _____

INFORMATION ON POOL: _____

OUTSIDE DECKS: _____

FENCES: _____

FRONT STOOP: _____

DRIVES & WALKS: _____

OTHER OUTSIDE PATIO, ETC:

SEPTIC TANK: _____

SUBCONTRACTOR: _____

WELL: _____

SUBCONTRACTOR: _____

SPRINKLER SYSTEM: _____

LANDSCAPING: _____

MAILBOX: _____

6.6 Sample Estimate Sheet

ESTIMATE SHEET

NAME: _____

DATE: _____

SQUARE FOOTAGE HOUSE / _____ / GARAGE _____

CODE	DESCRIPTION	ESTIMATED COST	NOTES
1000	CONCRETE		
2000	MASONRY-BLOCK		
203000	GLASS BLOCK		
2010	STONE		
2020	BRICK		
4000	ROUGH CARPENTRY		
5000	FINISH CARPENTRY		
5000	CUSTOM TRIM		
5010	STAIRS		
5020	WOOD SHELVING		
5030	WOOD CEILING		
6000	WATER PROOFING		
7000	INSULATION		
8000	ROOFING		
8010	BUILT UP ROOF		
9000	SHEET METAL		
9010	METAL SOFFIT/FACIA		
9020	GUTTERS		
10000	DOORS		

10010	FRONT DOOR		
10020	SLIDING GLASS DOORS		
10300	DOOR HARDWARE		
11000	WINDOWS		
12000	FIXED GLASS		
12010	MIRRORS		
13000	PLASTER/HARDCOTE		
14000	STUCCO		
15000	CERAMIC TILES		
15010	MARBLE SILLS		
15020	MARBLE VANITIES		
15030	MARBLE FLOORING		
17000	WOOD FLOORING		
18000	VINYL FLOORING		
19000	PAINTING		
19010	WALLPAPER		
20000	SPECIALTIES		
20010	MEDICINE CABINETS		
20020	VINYL SHELVING		
20030	IRONING BOARD		
20040	SKYLIGHTS		
20050	SHOWER DOORS/TUB		
21000	SECURITY SYSTEM		
21010	PREWIRE/TELE/CABLE		
21020	INTERCOM		
22000	CABINETS/VANITIES		

22100	BOOKCASES		
22020	WET BAR		
22030	BUILT INS		
23000	APPLIANCES		
25000	CARPET		
26000	SPECIAL CONSTRUCTION		
26010	FIREPLACE		
26020	GARAGE DOOR/OPENER		
26030	WOODEN DECKS		
26040	FENCES		
26050	SCREENED PORCH		
26051	SCREEN PORCH FLOOR		
26060	PLANTERS		
26070	POOL		
26080	MAILBOX		
26090	BARBECUE		
28000	PLUMBING/LABOR		
28011	PLUMBING/FIXTURES		
28010	SPA		
28020	SOLARS		
29000	HEAT/AC		
31000	ELECTRICAL/LABOR		
31010	ELECTRICAL/FIXTURE		
31020	ELECTRICAL FANS		
32000	GAS LINES		
35000	EARTH WORK/CLEAR		

36000	SITE UTILITIES/FEE		
36010	SEPTIC TANK		
36020	WELL		
37010	DRIVES AND WALKS		
37020	PATIO		
37030	FRONT STOOP		
37040	BUST CURBS		
39000	LAWNS AND PLANTING		
40000	UNUSUAL SITE CONSTR		
41010	CALLBACKS		
41020	VANDALISM/THEFT		
43000	PERMITS		
44000	HOW WARRANTY		
46000	SURVEY		
47000	LAYOUT		
55000	TEMPORARY GAS/ELEC		
56000	PORTI POTTI		
59000	TELEPHONE		
60000	CLEAN/REMOVE TRASH		
61000	FINAL CLEANUP		
81000	SALES COMMISSION		
82000	GENERAL OVERHEAD		
83000	A/E FEE AND DESIGN		
86000	OTHER FEES/SOIL TEST		
89000	BUILDERS RISK		

TOTAL ESTIMATE: _____

FOR OUR CUSTOMERS

**HERE IS A LIST OF "THINGS" TO DECIDE ON
DURING THE DIFFERENT STAGES OF CONSTRUCTION**

A) WHILE FOUNDATION IS UNDER CONSTRUCTION:

1. ELECTRICAL REQUIREMENTS IN THE SLAB-FLOOR PLUGS, ETC.
2. WINDOWS AND PATIO DOORS LOCATION, STYLE, SIZES, COLOR...
ANY CHANGES FROM PLANS.
3. WILL YOUR HOME HAVE A FIREPLACE? IF SO, WILL IT BE STANDARD
OR RAISED HEARTH TYPE? HOW HIGH WILL THE HEARTH BE? DO
YOU WANT A GAS LOG LIGHTER? IT'S NOT TOO EARLY TO BEGIN
THINKING ABOUT THE FINISH OF THE FIREPLACE. WILL YOU WANT
A MANTLE? WHAT TYPE AND STYLE? WHAT TYPE OF SURROUND?
MARBLE, BRICK, OR CERAMIC HEARTH, OR SOME OTHER TYPE?
4. TYPE OF PLUMBING FIXTURES (FAUCETS, WHIRLPOOL TUB, ETC.)
WHAT COLOR FIXTURES FOR ALL THE BATHS? KITCHEN SINK:
PORCELAIN OR STAINLESS STEEL? SIZE AND MODEL OF KITCHEN
SINK? ANY SPECIAL PLUMBING FIXTURES REQUIRED? KITCHEN SINK
FAUCET WITH SPRAY ATTACHMENT, SOAP DISPENSER, HOT WATER
DISPENSER?
5. WHAT MATERIALS ARE BEING USED ON THE EXTERIOR? DO YOU
WANT STAIN OR PAINT? WHAT COLORS?
6. WHAT COLOR OF TRIM FOR WINDOWS AND OUTSIDE DOORS?
7. DO YOU WANT A GAS LINE FOR CONNECTION FOR AN OUTSIDE
GRILL?
8. WHAT COLOR ROOF SHINGLES?
9. PICK CERAMIC TILE COLORS.
10. PICK FRONT DOOR STYLE.

B) WHEN WOOD FRAMING IS BEING STARTED:

1. WILL THERE BE ANY SPECIAL RECESSES OR BLOCKING IN THE
WALLS FOR SAFES, MEDICINE CABINETS, TOILET PAPER HOLDERS,
SHAMPOO WALL RECESSES, WALL NICHES, GRAB BARS, ETC.? IF SO,
WE NEED TO KNOW THE SIZES OF THE OPENINGS AND WHERE THEY
WILL BE LOCATED.

AFTER TRUSSES ARE SET, SKYLIGHT LOCATIONS CAN BE ACCURATELY DETERMINED.

2. ELECTRICAL:

YOU WILL BE ASKED TO MEET THE ELECTRICIAN AT THE HOUSE TO "SPOT" THE WALL PLUGS, SWITCHES, TV JACKS, PHONE JACKS, CABLE JACKS, RECESSED LIGHTS, ETC. PLEASE GIVE THIS YOUR ATTENTION. REMEMBER THAT IT IS FAR LESS EXPENSIVE TO INSTALL OUTLETS AT THIS TIME RATHER THAN LATER ON. THINK ABOUT THE RELATIONSHIP OF YOUR FURNITURE AND FURNISHINGS TO WALL PLUGS, LIGHTING, SWITCHES, ETC.

- a) THINK ABOUT ANY SPECIAL HEIGHTS THAT YOU WANT ELECTRICAL, PHONE, TV OUTLETS PLACED, I.E. TO ACCOMMODATE FURNISHINGS OR YOUR ELECTRIC/ELECTRONIC EQUIPMENT.**
- b) WILL YOU WANT ANY SPECIAL LIGHTS (SPOTS, RECESSED UNITS, OUTSIDE FLOOD LIGHTS)?**
- c) DO YOU WANT CEILING FANS, FANS WITH LIGHTS, OR JUST CEILING LIGHTS? CEILING FANS WITH LIGHTS TAKE SPECIAL WIRING. WHERE WILL THE FANS BE LOCATED?**
- d) WILL YOU REQUIRE ANY SPECIAL OUTLETS FOR STEREO SPEAKERS? IF SO, WHERE? EXTRA OUTLETS MAY BE ADDED CHARGE.**
- e) SECURITY SYSTEM SPECIAL REQUIREMENTS, IF ANY? SECURITY LIGHTING IF ANY?**

3. CABINETS:

- a) PICK OUT THE STYLE AND FINISH YOU LIKE. ARE THERE ANY SPECIAL CABINETS YOU DESIRE SUCH AS A LAZY SUSAN, WINE RACK, TRAY HOLDER, APPLIANCE GARAGE, ETC.?**
- b) SELECT BATHROOM AND LAUNDRY CABINETS, AS APPLICABLE.**
- c) PICK LAMINATE FOR KITCHEN, BATHS, LAUNDRY, BAR OR OTHER PLACES AS REQUIRED. LET US KNOW OF LAMINATE PRODUCT, COLOR, NUMBER, AND OTHER PERTINENT INFORMATION SUCH AS COUNTERTOP BEVEL EDGES, ETC.**

****NOTE: IN ORDER TO NOT HOLD UP CONSTRUCTION PROGRESS, CABINET SPECIFICATIONS MUST BE "FINALIZED" AS EARLY AS POSSIBLE ALONG WITH APPLIANCE SELECTION.**

C) WHEN INTERIOR WALL BOARD IS BEING HUNG:

1. WHAT COLOR STAIN OR PAINT DO YOU WANT ON YOUR WOODWORK?
2. WILL YOU WANT HARDCOAT SMOOTH OR TEXTURED? WHAT COLORS OF PAINT FOR THE WALLS AND CEILINGS?
3. WILL YOU WANT WALLPAPER ON ANY WALLS? WHERE? WALLPAPERING IS AN ALLOWANCE ITEM.
4. WHAT TYPE OF CORNER TREATMENT-ROUND OR 90 ?
5. ARE THERE ANY CHANGES IN INTERIOR CARPENTRY TRIM, DOORS, BASE, CROWN, ETC.?
6. **LIGHTING FIXTURES:**

FIXTURES MAY TAKE SEVERAL WEEKS TO ARRIVE AFTER BEING ORDERED. WE RECOMMEND THAT YOU SELECT THEM AS EARLY AS POSSIBLE.

THE FOLLOWING WILL HELP REMIND YOU OF WHAT LIGHT FIXTURES ARE TYPICALLY NEEDED:

- *the front door. On both sides or ceiling or both?
- *the overhead garage door. On both sides?
- *side garage door
- *back patio door
- *ceiling fans
- *bathroom lighting
- *any ceiling bedroom lights
- *foyer
- *kitchen
- *family room
- *dining room
- *closets
- *halls
- *special needs
- *living room
- *study
- *pool area
- *door chimes
- *laundry room ceiling
- *exterior
- *breakfast nook

LIGHTING FIXTURES, BULBS, ETC., ARE ALLOWANCE ITEMS SO TRY AND STAY CURRENT ON YOUR COSTS.

7. KITCHEN FIXTURES:

- a) **PICK OUT ALL APPLIANCES SO THEY CAN BE ORDERED. APPLIANCES TO THINK ABOUT: REFRIGERATOR, STOVE OR COOK TOP, SEPARATE MICROWAVE (REQUIRES SPECIAL WIRING), TRASH COMPACTOR, RANGE HOOD, DISHWASHER, DISPOSER, INSTANT HOT WATER, OVENS, WASHER, DRYER.**

REMEMBER THAT ALL APPLIANCE SELECTIONS SHOULD BE FINAL BEFORE CABINETS GO INTO PRODUCTION!!!

8. BATHROOMS:

- a) WE MUST KNOW OF ANY SPECIAL RECESSED ITEMS TO GO IN THESE ROOMS.
- b) WHAT TYPE, STYLE, & FINISH OF FAUCETS?
- c) MEDICINE CABINETS-WHAT SIZE, TYPE, STYLE?
- d) WHERE AND HOW MANY TOWEL BARS DO YOU NEED?
- e) ARE THERE TO BE SHOWER DOORS OR SHOWER CURTAIN RODS?
- f) WHAT TYPE, STYLE, COLOR, ETC., OF TOILETS.
- g) TYPE OF SHOWER, BATH VALVES, AND SHOWER HEADS; LOCATION OF SHOWER HEADS AND VALVES.

9. MISCELLANEOUS ITEMS:

- a) PICK OUT CARPET AND SHEET VINYL AS APPLICABLE.
- b) PICK OUT CERAMIC TILE AND GROUT COLOR FOR FOYER, BATHS, ETC.
- c) PICK OUT WALLPAPER AND GIVE US THE NAME OF THE BOOK, PAGE NUMBER, NAME, AND ANY OTHER PERTINENT INFORMATION TO HELP US ORDER THE CORRECT PAPER.
- d) WOOD FLOORING TYPE, FINISH, AND ANY OTHER PERTINENT INFORMATION.
- e) INTERVIEW LANDSCAPERS AND GET PROPOSALS AFTER COMPLETION OF HARDCOAT PLASTER.
- f) PICK OUT GARAGE DOOR.

WE HAVE NOT MEANT TO "MIND-BOGGLE" YOU, ONLY TO HELP YOU MAKE THESE CHOICES WELL IN ADVANCE OF WHEN THEY WILL BE NEEDED. PLEASE GIVE US ALL OF YOUR INFORMATION AS SOON AS POSSIBLE SO THAT ALL ITEMS CAN BE ORDERED IN TIME TO AVOID DELAYS.

CHAPTER 7

SUMMARY AND RECOMMENDATIONS

7.1 Summary

I accomplished exactly what I set out to when starting this report: I enhanced my technical engineering knowledge and gained valuable construction experience.

This report is a combination of the field work I conducted with MSPB, my academic studies over the past year, and several computer software applications. I have benefitted tremendously from this exercise, and the experience will pay great dividends in future duty assignments.

7.2 Recommendations

It would be very difficult to make recommendations concerning a highly successful business such as MSPB (the adage, "If it ain't broke don't fix it," definitely applies here).

One recommendation I did make was to utilize computer-driven project scheduling techniques. When I first started conducting research, I noticed that project schedules were not being generated for two major reasons. The first was lack of time and the second was schedules were not necessary. Clients were not interested in seeing elaborate schedules, they just wanted their houses to be built. As I mentioned in Chapter 5, the owner and construction superintendent have so much experience building homes, that planning/scheduling is done in their heads. Nevertheless, we developed a list of construction activities and scheduled a typical house using CPM 18 and Primavera. The results of this effort are contained in Chapter 5 and Appendices A through D. Although CPM 18 and Primavera are great time savers when compared to hand generating schedules, it takes a considerable amount of time to become proficient in their use. Since CPM 18 is

much easier to manipulate, and provided the owner with everything he needed, he chose it over Primavera. I would like to think that computer scheduling has helped the owner, but it probably has not been all that beneficial. The staff stays so busy performing regular duties that a schedule is more like a nicety than a necessity. The office has been doing business the same way for so long, that the time required to learn a new trick is not justified. As with all computer applications, if you do not continually use them, you tend to forget how they operate and have to learn the whole process over again.

My other recommendation would be to utilize computer-driven estimating software. This idea has great merit and would definitely save the owner a significant amount of time. The problem is I no longer have any time left - sounds like a good subject for next year's crop of graduate students to research.

APPENDIX A CLASSIC SCHEDULE REPORT

FEDSIONAL BUILDERS, INC.

PRIMAVERA PROJECT PLANNER

TYPICAL HOUSE CPM

ORT DATE 29JAN94 RUN NO. 7
8:45

START DATE 1NOV93 FIN DATE 21MAR94

SBIC SCHEDULE REPORT - SORT BY ES, TF

DATA DATE 1NOV93 PAGE NO. 1

ACTIVITY ID	ORIG DUR	REN. DUR	%	CODE	ACTIVITY DESCRIPTION	EARLY START	EARLY FINISH	LATE START	LATE FINISH	TOTAL FLOAT
10	7	7	0		OBTAIN BUILDING PERMIT	1NOV93	9NOV93	1NOV93	9NOV93	0
20	7	7	0		WATER METER	1NOV93	9NOV93	9NOV93	17NOV93	6
40	20	20	0		ORDER TRUSSES/WINDOWS	10NOV93	7DEC93	10NOV93	7DEC93	0
30	1	1	0		SURVEY	10NOV93	10NOV93	12NOV93	12NOV93	2
50	2	2	0		CLEAR/GNAB	11NOV93	12NOV93	15NOV93	16NOV93	2
60	1	1	0		STAKE OUT	15NOV93	15NOV93	17NOV93	17NOV93	2
70	3	3	0		POUR FOOTING	16NOV93	18NOV93	18NOV93	22NOV93	2
80	2	2	0		FOUNDATION BLOCK	19NOV93	22NOV93	23NOV93	24NOV93	2
90	1	1	0		SLAB FILL	23NOV93	23NOV93	25NOV93	25NOV93	2
100	1	1	0		SLAB PLUMBING/DRYER VENT	24NOV93	24NOV93	26NOV93	26NOV93	2
110	1	1	0		A/C CONDENSER LINES	25NOV93	25NOV93	29NOV93	29NOV93	2
120	1	1	0		SLAB ELECTRIC/JENN AIRE VENT	25NOV93	25NOV93	29NOV93	29NOV93	2
130	1	1	0		SOIL POISON	26NOV93	26NOV93	30NOV93	30NOV93	2
140	1	1	0		SLAB INSPECTION	29NOV93	29NOV93	1DEC93	1DEC93	2
150	2	2	0		POUR SLAB	30NOV93	1DEC93	2DEC93	3DEC93	2
170	2	2	0		EXTERIOR WALLS	2DEC93	3DEC93	6DEC93	7DEC93	2
160	2	2	0		WOODEN DECK	2DEC93	3DEC93	18FEB94	21FEB94	56
180	2	2	0		INTERIOR WALLS	6DEC93	7DEC93	23DEC93	24DEC93	13
200	2	2	0		HANG EXTERIOR SHEATHING	6DEC93	7DEC93	7FEB94	8FEB94	45
190	1	1	0		SET TRUSSES	8DEC93	8DEC93	8DEC93	8DEC93	0
220	4	4	0		STUCCO	8DEC93	13DEC93	9FEB94	14FEB94	45
230	15	15	0		BRICK/STONE	8DEC93	28DEC93	11FEB94	3MAR94	47
210	1	1	0		FASCIA	9DEC93	9DEC93	9DEC93	9DEC93	0
240	4	4	0		DRY-IN	10DEC93	15DEC93	10DEC93	15DEC93	0
290	6	6	0		ROUGH ELECTRICAL	16DEC93	23DEC93	16DEC93	23DEC93	0
260	4	4	0		A/C DUCT WORK	16DEC93	21DEC93	23DEC93	28DEC93	5
250	2	2	0		PLUMBING STACK-OUT	16DEC93	17DEC93	27DEC93	28DEC93	7
280	1	1	0		SET WINDOWS	16DEC93	16DEC93	9FEB94	9FEB94	39
270	1	1	0		FIXED GLASS	16DEC93	16DEC93	17MAR94	17MAR94	65
300	3	3	0		SIDING	17DEC93	21DEC93	10FEB94	14FEB94	39

FEDERSON BUILDERS, INC.

PRIMAVERA PROJECT PLANNER

TYPICAL HOUSE CPM

ORT DATE 29JAN94 RUN NO. 7

START DATE 1NOV93 FIN DATE 21MAR94

8:45

SSIC SCHEDULE REPORT - SORT BY ES, TF

DATA DATE 1NOV93 PAGE NO. 2

ACTIVITY ID	ORIG DUR	REM DUR	%	CODE	ACTIVITY DESCRIPTION	EARLY START	EARLY FINISH	LATE START	LATE FINISH	TOTAL FLOAT
350	3	3	0		EXTERIOR PAINT	22DEC93	24DEC93	15FEB94	17FEB94	39
330	3	3	0		ROOFING	24DEC93	28DEC93	24DEC93	28DEC93	0
310	1	1	0		SECURITY PRE-WIRE	24DEC93	24DEC93	17MAR94	17MAR94	59
320	1	1	0		STEREO/TV/INTERCOM PRE-WIRE	24DEC93	24DEC93	17MAR94	17MAR94	59
390	2	2	0		PORCH SCREENING	27DEC93	28DEC93	18FEB94	21FEB94	39
360	1	1	0		SECURITY TRIM	27DEC93	27DEC93	18MAR94	18MAR94	59
370	1	1	0		STEREO/TV/INTERCOM TRIM	27DEC93	27DEC93	18MAR94	18MAR94	59
380	1	1	0		FRAMING INSPECTION	29DEC93	29DEC93	29DEC93	29DEC93	0
340	3	3	0		SOFFIT	29DEC93	31DEC93	4MAR94	8MAR94	47
400	2	2	0		INSULATION	30DEC93	31DEC93	30DEC93	31DEC93	0
410	7	7	0		HANG GYP-BOARD	3JAN94	11JAN94	3JAN94	11JAN94	0
420	4	4	0		HARDCOTE	12JAN94	17JAN94	12JAN94	17JAN94	0
440	25	25	0		SWIMMING POOL	18JAN94	21FEB94	18JAN94	21FEB94	0
430	4	4	0		FINISH CARPENTRY	18JAN94	21JAN94	10FEB94	15FEB94	17
460	7	7	0		CERAMIC TILE/WINDOW SILL	18JAN94	26JAN94	2MAR94	10MAR94	31
450	1	1	0		GARAGE DOOR	18JAN94	18JAN94	4MAR94	4MAR94	33
480	6	6	0		PAINT INTERIOR	24JAN94	31JAN94	16FEB94	23FEB94	17
490	1	1	0		SET ELECTRICAL PANEL/LOCK HOUSE	24JAN94	24JAN94	4MAR94	4MAR94	29
470	1	1	0		MEDICINE CABINET	24JAN94	24JAN94	10MAR94	10MAR94	33
530	2	2	0		SEMI-PERM ELECTRIC	25JAN94	26JAN94	7MAR94	8MAR94	29
520	5	5	0		CABINETS/VANITIES	1FEB94	7FEB94	24FEB94	2MAR94	17
510	1	1	0		FIRE-PLACE VENEER	1FEB94	1FEB94	15MAR94	15MAR94	30
550	1	1	0		APPLIANCES	8FEB94	8FEB94	3MAR94	3MAR94	17
560	5	5	0		WALLPAPER	8FEB94	14FEB94	7MAR94	11MAR94	19
590	3	3	0		PLUMBING TRIM	9FEB94	11FEB94	4MAR94	8MAR94	17
600	1	1	0		MIRRORS	15FEB94	15FEB94	14MAR94	14MAR94	19
650	1	1	0		SHOWER DOORS	16FEB94	16FEB94	15MAR94	15MAR94	19
500	2	2	0		SITE CLEAN-UP	22FEB94	23FEB94	22FEB94	23FEB94	0
540	2	2	0		FINAL GRADE	24FEB94	25FEB94	24FEB94	25FEB94	0
570	1	1	0		A/C PADS	28FEB94	28FEB94	28FEB94	28FEB94	0

PROFESSIONAL BUILDERS, INC.

PRIMAVERA PROJECT PLANNER

TYPICAL HOUSE CPM

RT DATE 29JUN94 RUN NO. 7
8:45


START DATE 1NOV93 FIN DATE 21MAR94


SIC SCHEDULE REPORT - SORT BY ES, TF


DATA DATE 1NOV93 PAGE NO. 3


ACTIVITY ID	ORIG DUR	REN DUR	%	CODE	ACTIVITY DESCRIPTION	EARLY START	EARLY FINISH	LATE START	LATE FINISH	TOTAL FLOAT
580	3	3	0		DRIVEWAY/SIDEWALK	28FEB94	2MAR94	4MAR94	8MAR94	4
610	3	3	0		HVAC TRIM	1MAR94	3MAR94	1MAR94	3MAR94	0
640	5	5	0		ELECTRICAL TRIM	1MAR94	7MAR94	9MAR94	15MAR94	6
630	8	8	0		LANDSCAPE	3MAR94	14MAR94	9MAR94	18MAR94	4
620	3	3	0		CARPET/VINYL FLOORING	3MAR94	7MAR94	11MAR94	15MAR94	6
660	8	8	0		WOOD FLOORING	4MAR94	15MAR94	4MAR94	15MAR94	0
670	3	3	0		HOUSE CLEAN-UP	16MAR94	18MAR94	16MAR94	18MAR94	0
680	1	1	0		FINAL INSPECTION	21MAR94	21MAR94	21MAR94	21MAR94	0

APPENDIX B TIME-SCALED LOGIC DIAGRAM

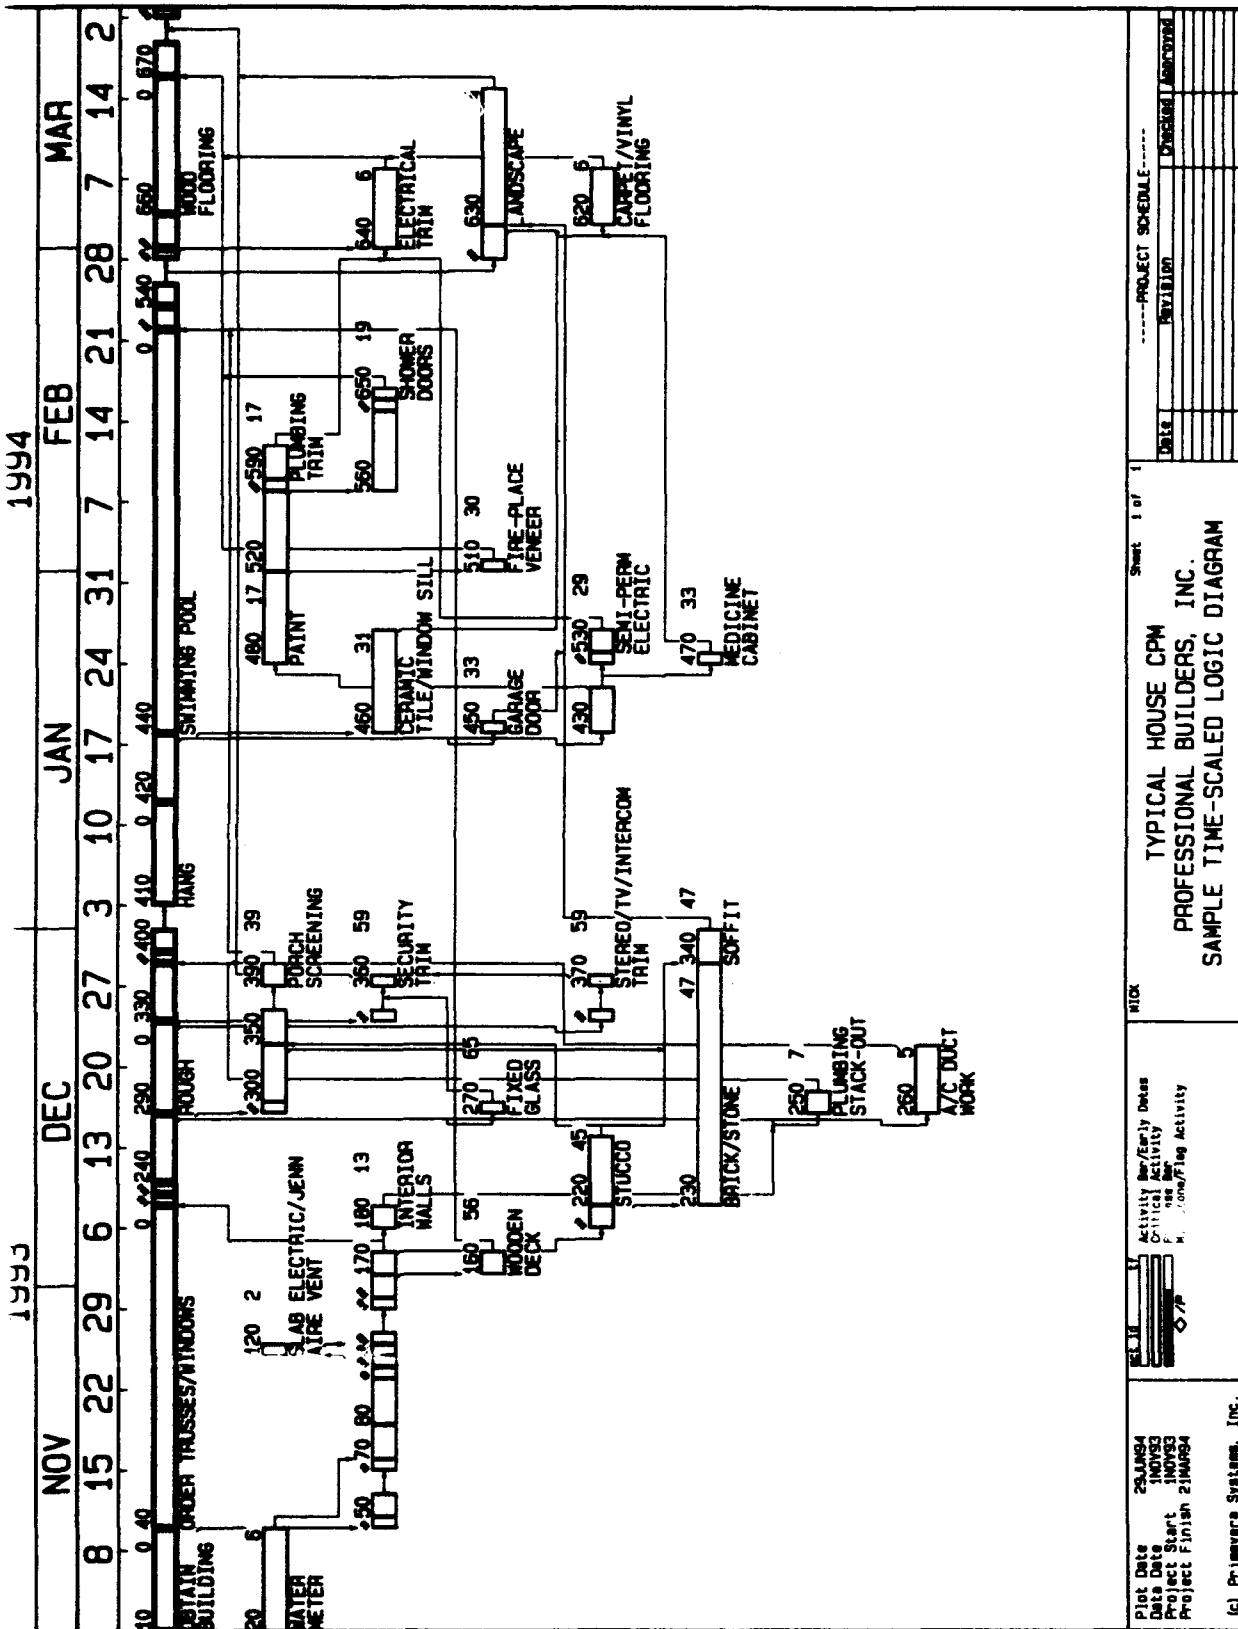

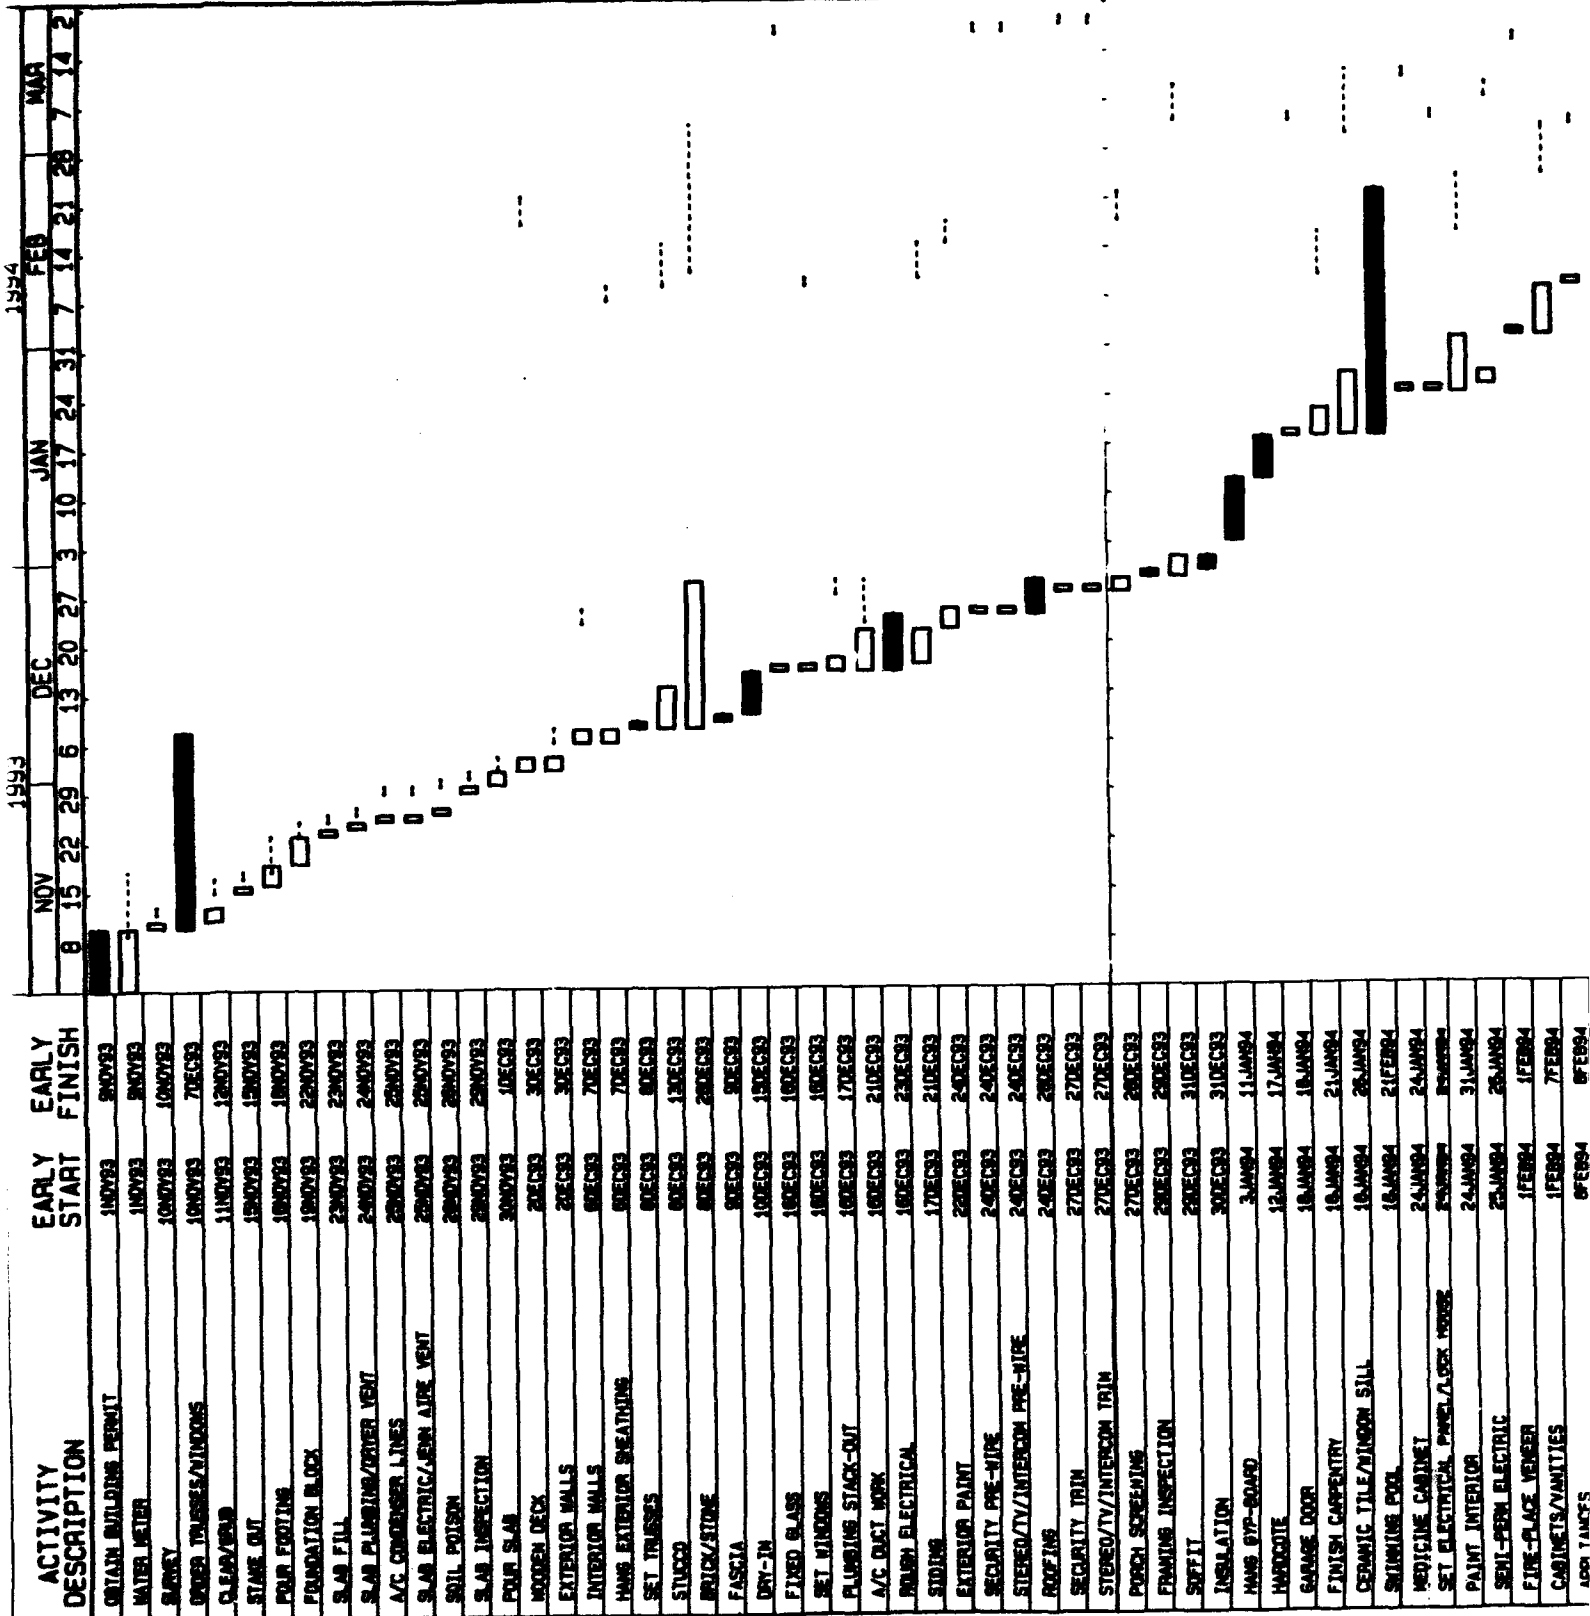

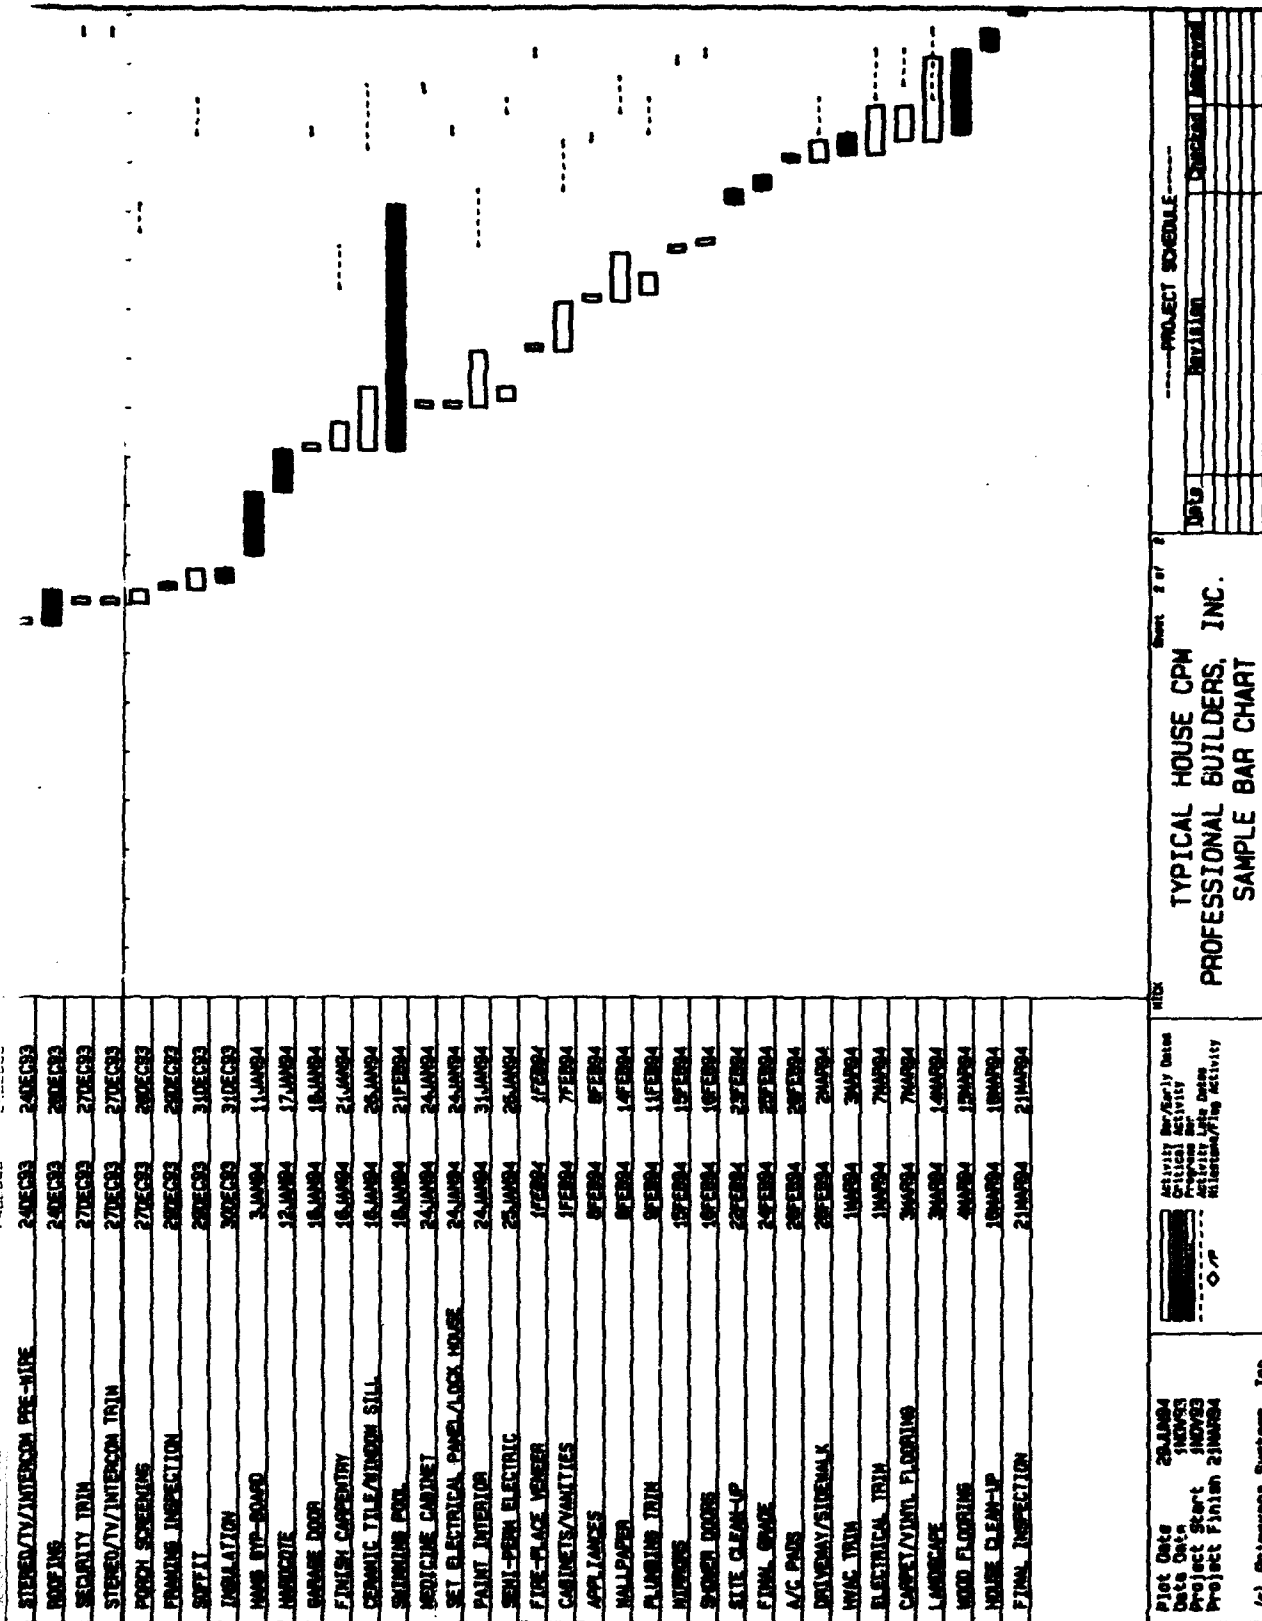

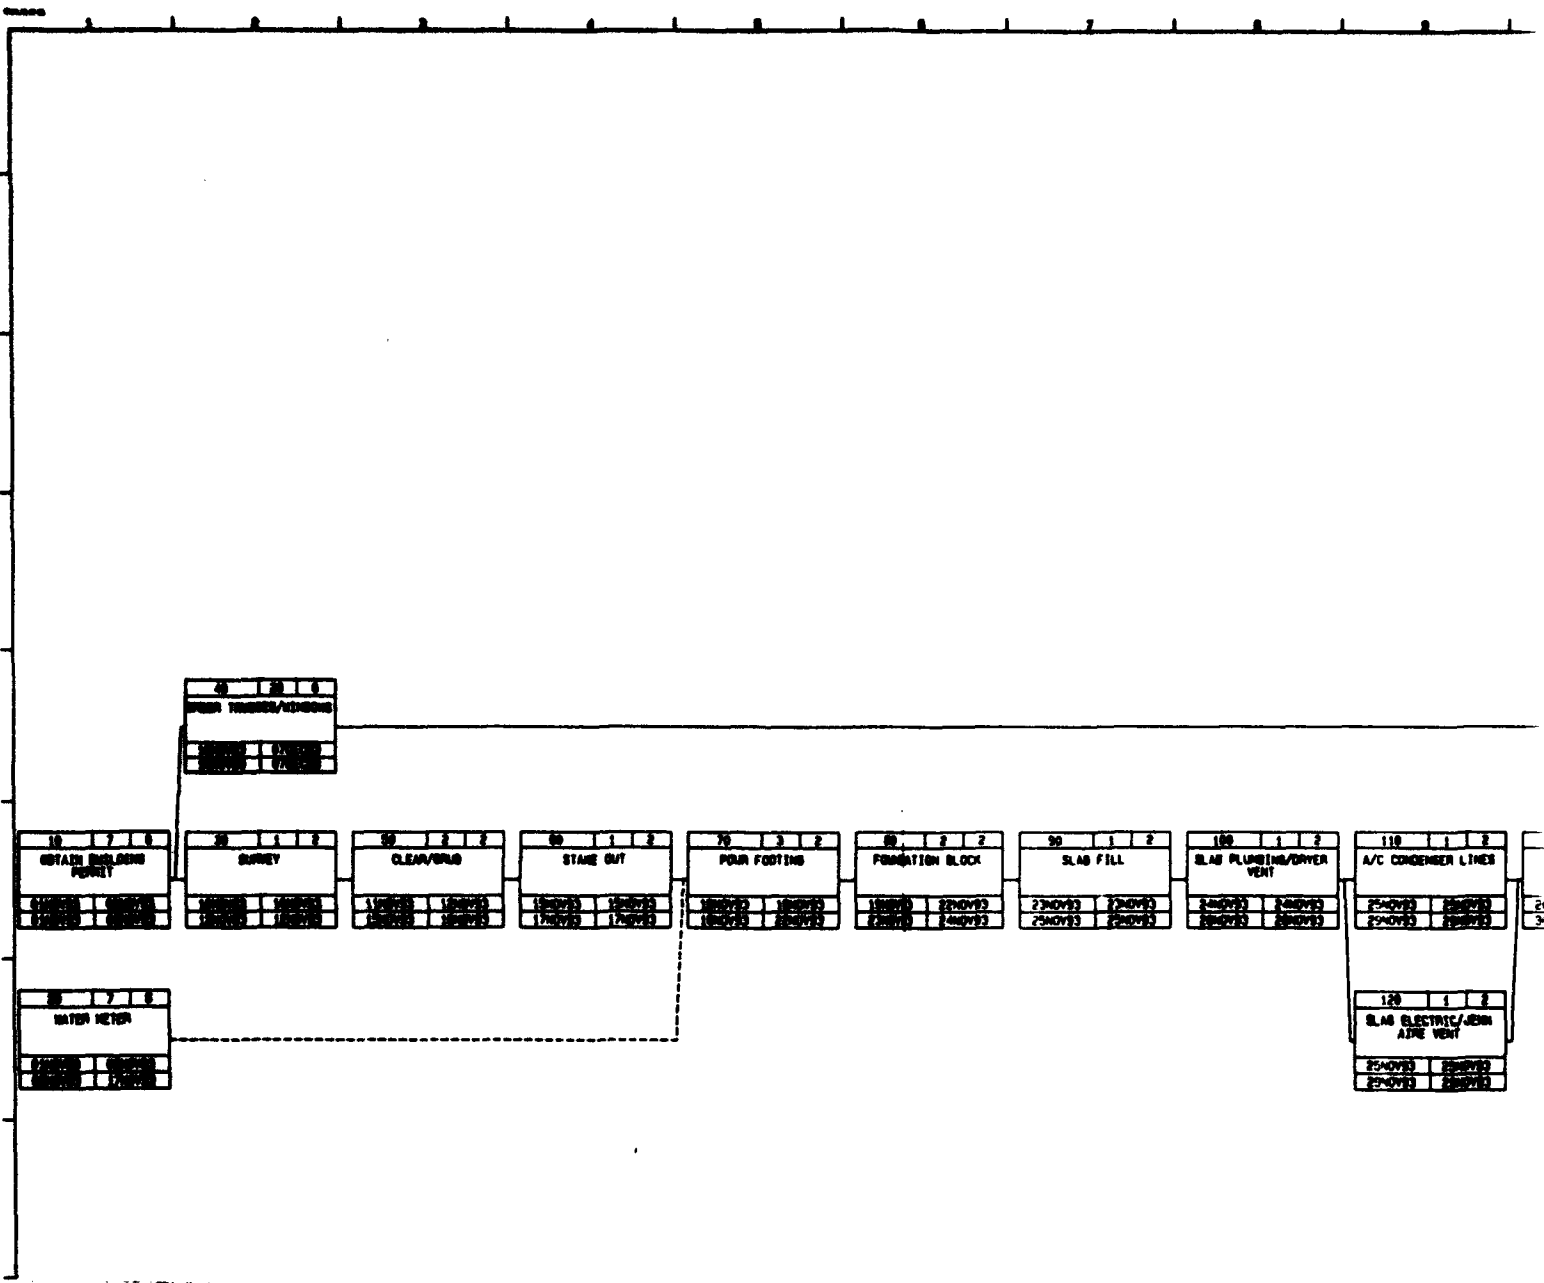

4	1	2	3
1	2	3	4
5	6	7	8

10	1	2	3
1	2	3	4
5	6	7	8

20	1	2	3
1	2	3	4
5	6	7	8

30	1	2	3
1	2	3	4
5	6	7	8

40	1	2	3
1	2	3	4
5	6	7	8

50	1	2	3
1	2	3	4
5	6	7	8

60	1	2	3
1	2	3	4
5	6	7	8

70	1	2	3
1	2	3	4
5	6	7	8

80	1	2	3
1	2	3	4
5	6	7	8

90	1	2	3
1	2	3	4
5	6	7	8

100	1	2	3
1	2	3	4
5	6	7	8

10	1	2	3
1	2	3	4
5	6	7	8

120	1	2	3
1	2	3	4
5	6	7	8

2

100	1	2
SLAB PLUMBING/DRYER VENT		
200000	200000	200000
200000	200000	200000

110	1	2
A/C CONDENSER LINES		
200000	200000	200000
200000	200000	200000

120	1	2
SLAB ELECTRIC/IGN AIR VENT		
200000	200000	200000
200000	200000	200000

130	1	2
SOIL PIPING		
200000	200000	200000
200000	200000	200000

140	1	2
SLAB REJECTION		
200000	200000	200000
010000	010000	010000

150	2	2
POUR SLAB		
200000	010000	010000
000000	000000	000000

170	2	2
EXTERIOR WALLS		
000000	000000	000000
000000	000000	000000

200	1	0
SET TRUSSES		
000000	000000	000000
000000	000000	000000

210	1	0
FABRIC		
000000	000000	000000
000000	000000	000000

240	4	0
DRY-IN		
100000	150000	150000
100000	150000	150000

290		
ROOF		
100000		
100000		

200	2	0
INTERIOR WALLS		
000000	000000	000000
000000	000000	000000

250		
PLUMB		
000000		
000000		

200	15	47
TICK/STONE		
000000	000000	000000
000000	000000	000000

280		
SI		
100000		
000000		

3

270	1	00
FINISH GLASS		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

300	1	50
SECURITY TRIM		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

450	7	31
CERAMIC TILE/FLOORING		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

310	1	50
SECURITY PRE-WIRE		
240CS3	240CS3	240CS3
1700CS4	1700CS4	1700CS4

200	4	5
A/C DUCT WORK		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

400	1	33
GARAGE DOOR		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

1	0	
RUBBER		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

210	1	0
FASCIA		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

240	4	0
DRY-IN		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

200	0	0
ROUGH ELECTRICAL		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

330	3	0
ROOFING		
240CS3	240CS3	240CS3
240CS3	240CS3	240CS3

300	1	0
FRAMING INSPECTION		
240CS3	240CS3	240CS3
240CS3	240CS3	240CS3

400	2	0
INSULATION		
300CS3	310CS3	300CS3
300CS3	310CS3	300CS3

410	7	0
HAND DYP-BOARD		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

420	4	0
HARDWOTE		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

430	4	17
FINISH CARPENTRY		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

300	1	50
STEREO/TV/INTERCOM PRE-WIRE		
240CS3	240CS3	240CS3
1700CS4	1700CS4	1700CS4

370	1	53
STEREO/TV/INTERCOM TRIM		
240CS3	240CS3	240CS3
1700CS4	1700CS4	1700CS4

200	0	7
PLUMBING STACK OUT		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

2	13	
H WALLS		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

200	1	37
SET HANDING		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

200	3	30
STAIRING		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

2	15	47
STAIR/STAIR		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

440	25	0
STAIRING FLOOR		
1000CS3	1000CS3	1000CS3
1000CS3	1000CS3	1000CS3

450	7	8
CERAMIC TILE/WINDOW SILL		
18 JAN 94	24 JAN 94	
07 MAR 94	10 MAR 94	

680	3	8
CARPET/VINYL FLOORING		
07 MAR 94	07 MAR 94	
10 MAR 94	10 MAR 94	

470	1	33
MEDICINE CABINET		
24 JAN 94	24 JAN 94	
10 MAR 94	10 MAR 94	

490	1	33
GARAGE DOOR		
18 JAN 94	18 JAN 94	
04 MAR 94	04 MAR 94	

530	2	33
SEMI-PERM ELECTRICAL		
24 JAN 94	24 JAN 94	
07 MAR 94	07 MAR 94	

430	1	29
SET ELECTRICAL PANEL / LICK HOUSE		
24 JAN 94	24 JAN 94	
04 MAR 94	04 MAR 94	

7	8	
NO DWP-BOARD		
11 JAN 94	11 JAN 94	
11 JAN 94	11 JAN 94	

420	4	8
HARDWARE		
12 JAN 94	17 JAN 94	
17 JAN 94	17 JAN 94	

430	4	17
FINISH CARPENTRY		
18 JAN 94	21 JAN 94	
10 FEB 94	10 FEB 94	

480	6	17
PAINT INTERIOR		
24 JAN 94	31 JAN 94	
10 FEB 94	27 FEB 94	

520	5	17
CABINETS/VANITIES		
07 FEB 94	07 FEB 94	
24 FEB 94	02 MAR 94	

500	1	17
APPLIANCES		
07 FEB 94	07 FEB 94	
02 MAR 94	02 MAR 94	

580	3	17
PLUMBING TRIM		
07 FEB 94	11 FEB 94	
04 MAR 94	04 MAR 94	

640	8	8
ELECTRICAL TRIM		
07 MAR 94	07 MAR 94	
02 APR 94	10 MAR 94	

670	3	8
HOUSE CLEAN-UP		
10 MAR 94	10 MAR 94	
10 MAR 94	10 MAR 94	

680	1	8
FINAL INSPECTION		
11 MAR 94	11 MAR 94	
11 MAR 94	11 MAR 94	

500	5	13
WALLPAPER		
07 FEB 94	14 FEB 94	
07 MAR 94	11 MAR 94	

600	1	13
KITCHEN		
10 FEB 94	10 FEB 94	
10 MAR 94	10 MAR 94	

650	1	13
BATHROOM		
10 FEB 94	10 FEB 94	
10 MAR 94	10 MAR 94	

510	1	30
FIRE-PLACE VENEER		
07 FEB 94	07 FEB 94	
10 MAR 94	10 MAR 94	

440	1	8
SWIMMING POOL		
11 MAR 94	11 MAR 94	
11 MAR 94	11 MAR 94	

570	1	8
A/C PADS		
11 MAR 94	11 MAR 94	
11 MAR 94	11 MAR 94	

610	3	8
HVAC TRIM		
11 MAR 94	11 MAR 94	
11 MAR 94	11 MAR 94	

660	1	8
WOOD FLOORING		
11 MAR 94	11 MAR 94	
11 MAR 94	11 MAR 94	

4

5

60	3	0
CARPET/VINYL FLOORING		
000000	000000	000000
000000	000000	000000

17
16
15
14
13
12
11
10
9
8
7
6
5
4
3
2
1

500	1	17
APPLIANCES		
000000	000000	000000
000000	000000	000000

500	3	17
PLUMBING TRIM		
000000	000000	000000
000000	000000	000000

640	3	0
ELECTRICAL TRIM		
000000	000000	000000
000000	000000	000000

670	3	0
HOUSE CLEAN-UP		
000000	000000	000000
000000	000000	000000

600	1	0
FINAL INSPECTION		
000000	000000	000000
000000	000000	000000

500	5	17
WALLPAPER		
000000	000000	000000
000000	000000	000000

500	1	17
KITCHEN		
000000	000000	000000
000000	000000	000000


500	1	17
BATHROOM		
000000	000000	000000
000000	000000	000000

30
29
28
27
26
25
24
23
22
21
20
19
18
17
16
15
14
13
12
11
10
9
8
7
6
5
4
3
2
1

500	1	0
A/C PRBS		
000000	000000	000000


500	3	0
HOUSE TRIM		
000000	000000	000000

500	3	0
WOOD FLOORING		
000000	000000	000000

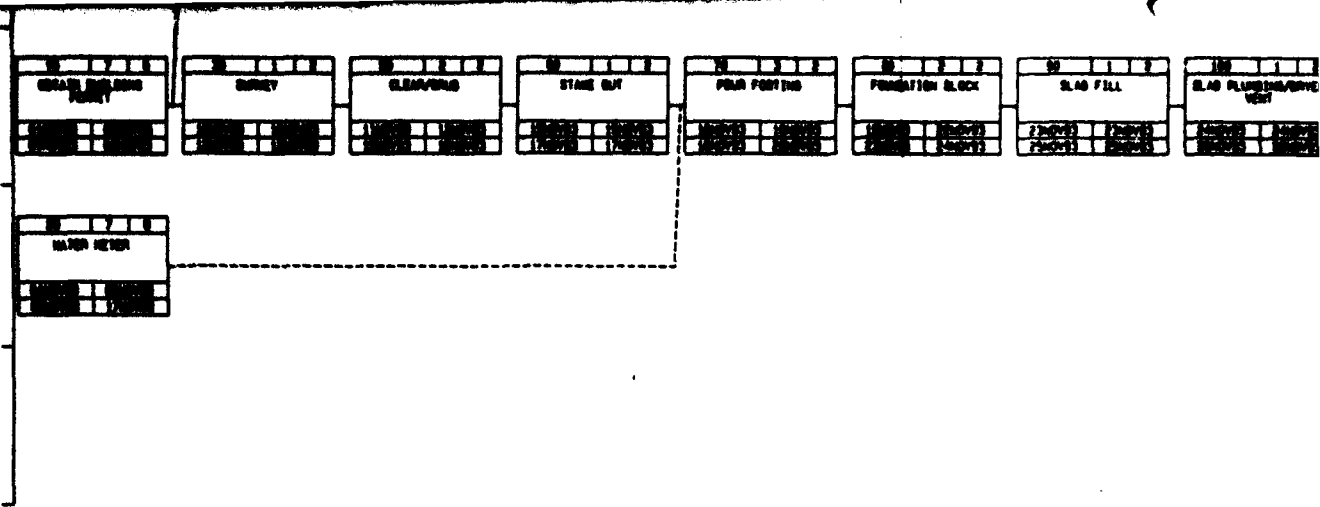


①

100	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	61	62	63	64	65	66	67	68	69	70	71	72	73	74	75	76	77	78	79	80	81	82	83	84	85	86	87	88	89	90	91	92	93	94	95	96	97	98	99	100	101	102	103	104	105	106	107	108	109	110	111	112	113	114	115	116	117	118	119	120	121	122	123	124	125	126	127	128	129	130	131	132	133	134	135	136	137	138	139	140	141	142	143	144	145	146	147	148	149	150	151	152	153	154	155	156	157	158	159	160	161	162	163	164	165	166	167	168	169	170	171	172	173	174	175	176	177	178	179	180	181	182	183	184	185	186	187	188	189	190	191	192	193	194	195	196	197	198	199	200	201	202	203	204	205	206	207	208	209	210	211	212	213	214	215	216	217	218	219	220	221	222	223	224	225	226	227	228	229	230	231	232	233	234	235	236	237	238	239	240	241	242	243	244	245	246	247	248	249	250	251	252	253	254	255	256	257	258	259	260	261	262	263	264	265	266	267	268	269	270	271	272	273	274	275	276	277	278	279	280	281	282	283	284	285	286	287	288	289	290	291	292	293	294	295	296	297	298	299	300	301	302	303	304	305	306	307	308	309	310	311	312	313	314	315	316	317	318	319	320	321	322	323	324	325	326	327	328	329	330	331	332	333	334	335	336	337	338	339	340	341	342	343	344	345	346	347	348	349	350	351	352	353	354	355	356	357	358	359	360	361	362	363	364	365	366	367	368	369	370	371	372	373	374	375	376	377	378	379	380	381	382	383	384	385	386	387	388	389	390	391	392	393	394	395	396	397	398	399	400	401	402	403	404	405	406	407	408	409	410	411	412	413	414	415	416	417	418	419	420	421	422	423	424	425	426	427	428	429	430	431	432	433	434	435	436	437	438	439	440	441	442	443	444	445	446	447	448	449	450	451	452	453	454	455	456	457	458	459	460	461	462	463	464	465	466	467	468	469	470	471	472	473	474	475	476	477	478	479	480	481	482	483	484	485	486	487	488	489	490	491	492	493	494	495	496	497	498	499	500	501	502	503	504	505	506	507	508	509	510	511	512	513	514	515	516	517	518	519	520	521	522	523	524	525	526	527	528	529	530	531	532	533	534	535	536	537	538	539	540	541	542	543	544	545	546	547	548	549	550	551	552	553	554	555	556	557	558	559	560	561	562	563	564	565	566	567	568	569	570	571	572	573	574	575	576	577	578	579	580	581	582	583	584	585	586	587	588	589	590	591	592	593	594	595	596	597	598	599	600	601	602	603	604	605	606	607	608	609	610	611	612	613	614	615	616	617	618	619	620	621	622	623	624	625	626	627	628	629	630	631	632	633	634	635	636	637	638	639	640	641	642	643	644	645	646	647	648	649	650	651	652	653	654	655	656	657	658	659	660	661	662	663	664	665	666	667	668	669	670	671	672	673	674	675	676	677	678	679	680	681	682	683	684	685	686	687	688	689	690	691	692	693	694	695	696	697	698	699	700	701	702	703	704	705	706	707	708	709	710	711	712	713	714	715	716	717	718	719	720	721	722	723	724	725	726	727	728	729	730	731	732	733	734	735	736	737	738	739	740	741	742	743	744	745	746	747	748	749	750	751	752	753	754	755	756	757	758	759	760	761	762	763	764	765	766	767	768	769	770	771	772	773	774	775	776	777	778	779	780	781	782	783	784	785	786	787	788	789	790	791	792	793	794	795	796	797	798	799	800	801	802	803	804	805	806	807	808	809	810	811	812	813	814	815	816	817	818	819	820	821	822	823	824	825	826	827	828	829	830	831	832	833	834	835	836	837	838	839	840	841	842	843	844	845	846	847	848	849	850	851	852	853	854	855	856	857	858	859	860	861	862	863	864	865	866	867	868	869	870	871	872	873	874	875	876	877	878	879	880	881	882	883	884	885	886	887	888	889	890	891	892	893	894	895	896	897	898	899	900	901	902	903	904	905	906	907	908	909	910	911	912	913	914	915	916	917	918	919	920	921	922	923	924	925	926	927	928	929	930	931	932	933	934	935	936	937	938	939	940	941	942	943	944	945	946	947	948	949	950	951	952	953	954	955	956	957	958	959	960	961	962	963	964	965	966	967	968	969	970	971	972	973	974	975	976	977	978	979	980	981	982	983	984	985	986	987	988	989	990	991	992	993	994	995	996	997	998	999	1000	1001	1002	1003	1004	1005	1006	1007	1008	1009	1010	1011	1012	1013	1014	1015	1016	1017	1018	1019	1020	1021	1022	1023	1024	1025	1026	1027	1028	1029	1030	1031	1032	1033	1034	1035	1036	1037	1038	1039	1040	1041	1042	1043	1044	1045	1046	1047	1048	1049	1050	1051	1052	1053	1054	1055	1056	1057	1058	1059	1060	1061	1062	1063	1064	1065	1066	1067	1068	1069	1070	1071	1072	1073	1074	1075	1076	1077	1078	1079	1080	1081	1082	1083	1084	1085	1086	1087	1088	1089	1090	1091	1092	1093	1094	1095	1096	1097	1098	1099	1100	1101	1102	1103	1104	1105	1106	1107	1108	1109	1110	1111	1112	1113	1114	1115	1116	1117	1118	1119	1120	1121	1122	1123	1124	1125	1126	1127	1128	1129	1130	1131	1132	1133	1134	1135	1136	1137	1138	1139	1140	1141	1142	1143	1144	1145	1146	1147	1148	1149	1150	1151	1152	1153	1154	1155	1156	1157	1158	1159	1160	1161	1162	1163	1164	1165	1166	1167	1168	1169	1170	1171	1172	1173	1174	1175	1176	1177	1178	1179	1180	1181	1182	1183	1184	1185	1186	1187	1188	1189	1190	1191	1192	1193	1194	1195	1196	1197	1198	1199	1200	1201	1202	1203	1204	1205	1206	1207	1208	1209	1210	1211	1212	1213	1214	1215	1216	1217	1218	1219	1220	1221	1222	1223	1224	1225	1226	1227	1228	1229	1230	1231	1232	1233	1234	1235	1236	1237	1238	1239	1240	1241	1242	1243	1244	1245	1246	1247	1248	1249	1250	1251	1252	1253	1254	1255	1256	1257	1258	1259	1260	1261	1262	1263	1264	1265	1266	1267	1268	1269	1270	1271	1272	1273	1274	1275	1276	1277	1278	1279	1280	1281	1282	1283	1284	1285	1286	1287	1288	1289	1290	1291	1292	1293	1294	1295	1296	1297	1298	1299	1300	1301	1302	1303	1304	1305	1306	1307	1308	1309	1310	1311	1312	1313	1314	1315	1316	1317	1318	1319	1320	1321	1322	1323	1324	1325	1326	1327	1328	1329	1330	1331	1332	1333	1334	1335	1336	1337	1338	1339	1340	1341	1342	1343	1344	1345	1346	1347	1348	1349	1350	1351	1352	1353	1354	1355	1356	1357	1358	1359	1360	1361	1362	1363	1364	1365	1366	1367	1368	1369	1370	1371	1372	1373	1374	1375	1376	1377	1378	1379	1380	1381	1382	1383	1384	1385	1386	1387	1388	1389	1390	1391	1392	1393	1394	1395	1396	1397	1398	1399	1400	1401	1402	1403	1404	1405	1406	1407	1408	1409	1410	1411	1412	1413	1414	1415	1416	1417	1418	1419	1420	1421	1422	1423	1424	1425	1426	1427	1428	1429	1430	1431	1432	1433	1434	1435	1436	1437	1438	1439	1440	1441	1442	1443	1444	1445	1446	1447	1448	1449	1450	1451	1452	1453	1454	1455	1456	1457	1458	1459	1460	1461	1462	1463	1464	1465	1466	1467	1468	1469	1470	1471	1472	1473	1474	1475	1476	1477	1478	1479	1480	1481	1482	1483	1484	1485	1486	1487	1488	1489	1490	1491	1492	1493	1494	1495</
-----	---	---	---	---	---	---	---	---	---	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	------	--------

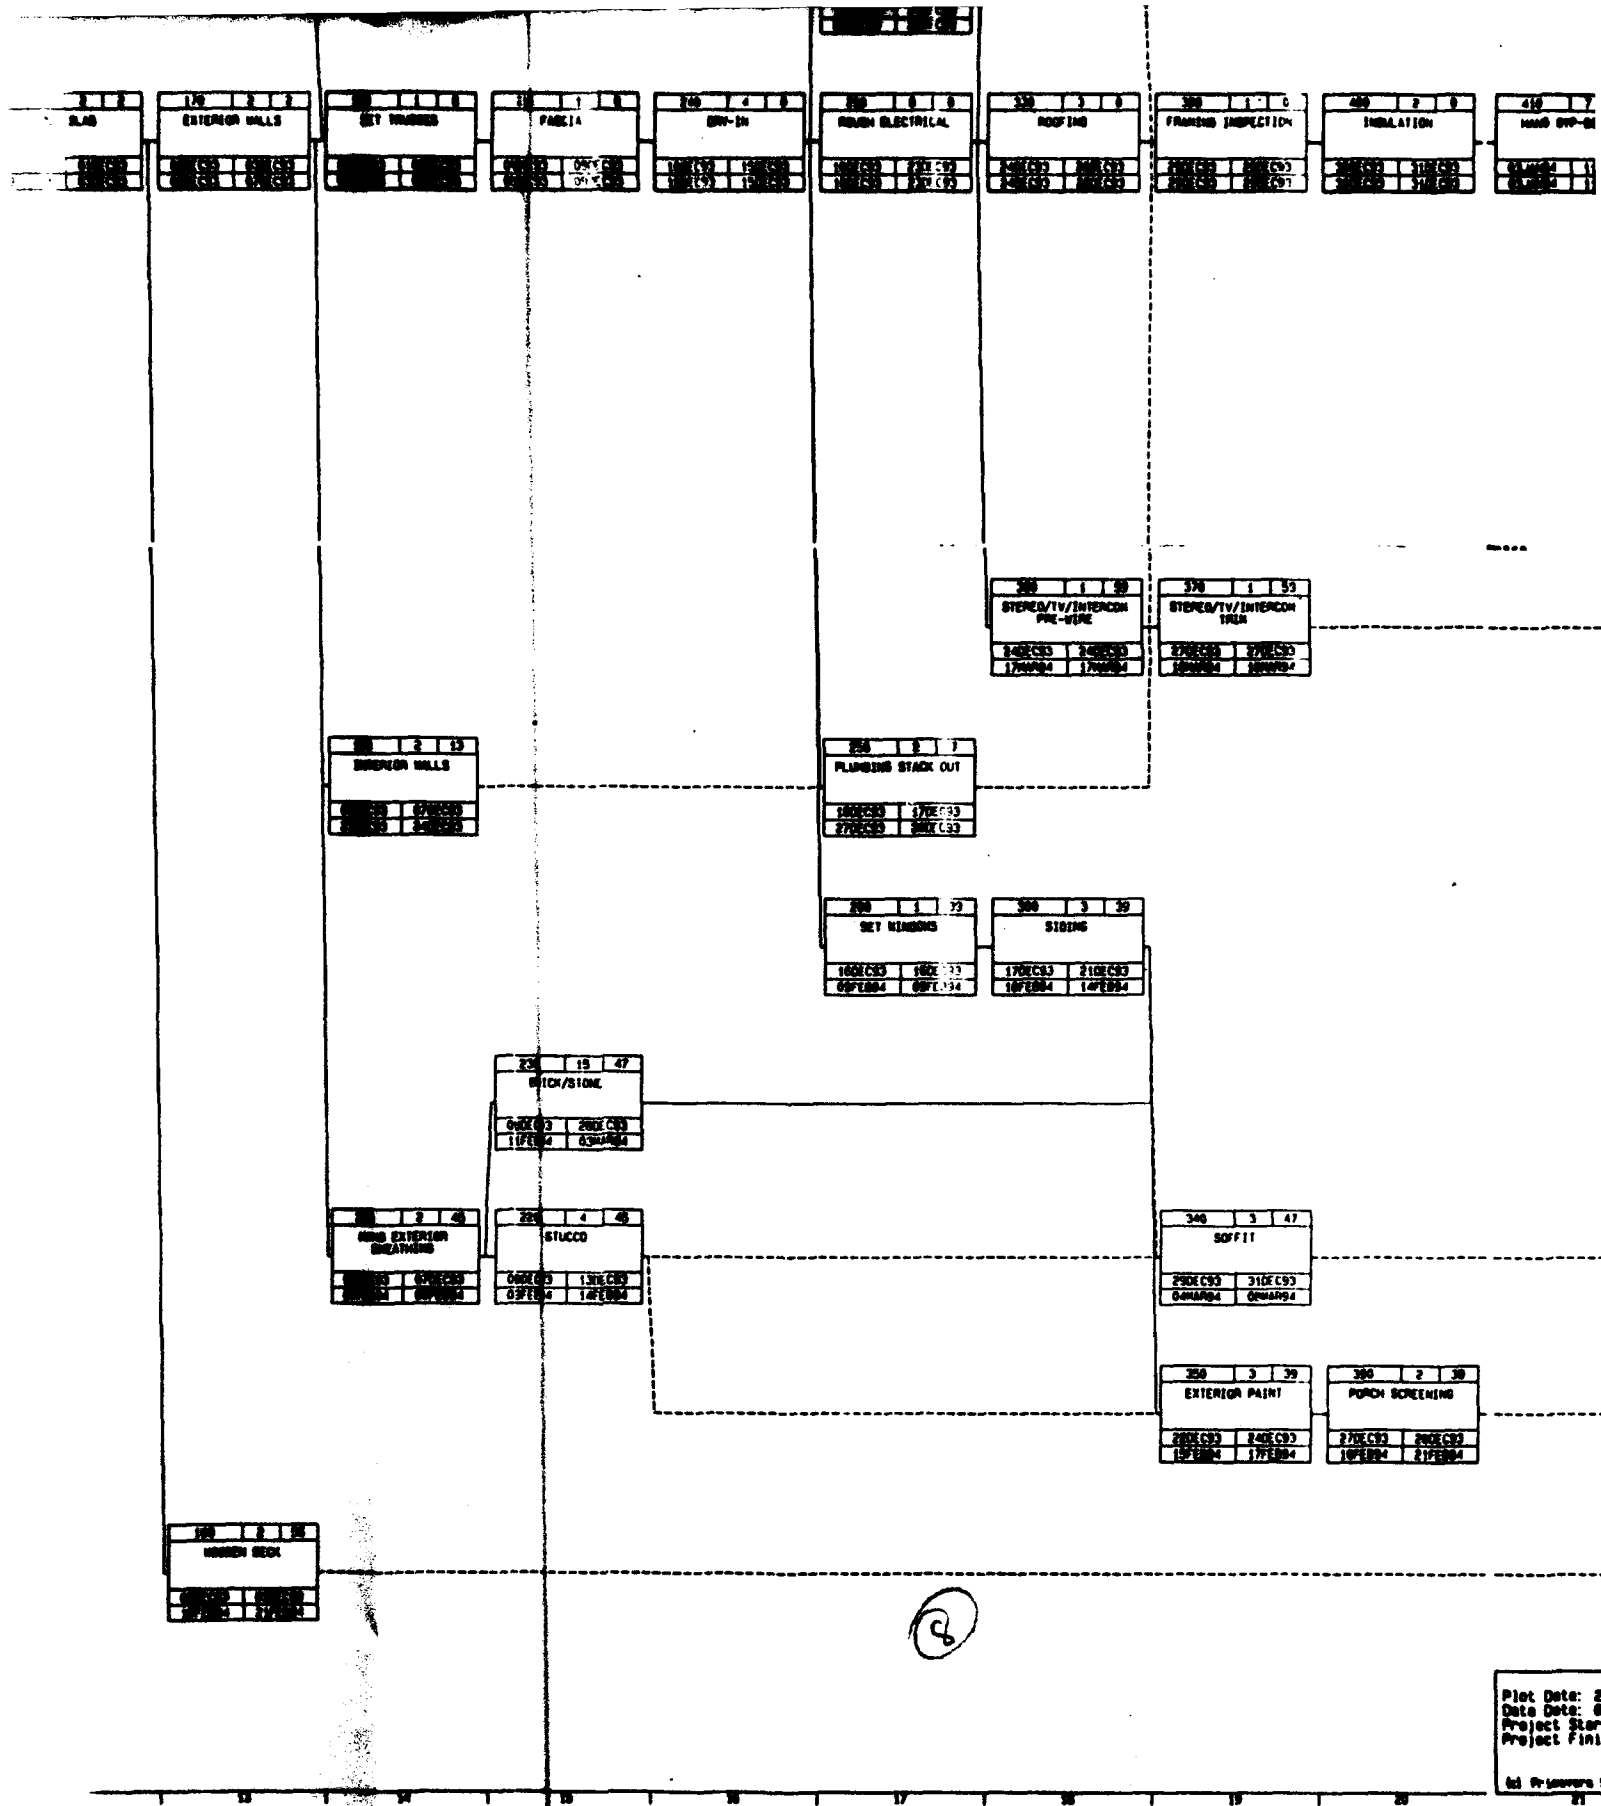

Plot Date: 28
 Date Data: 01
 Project Start
 Project Finish
 1st Primavera 9

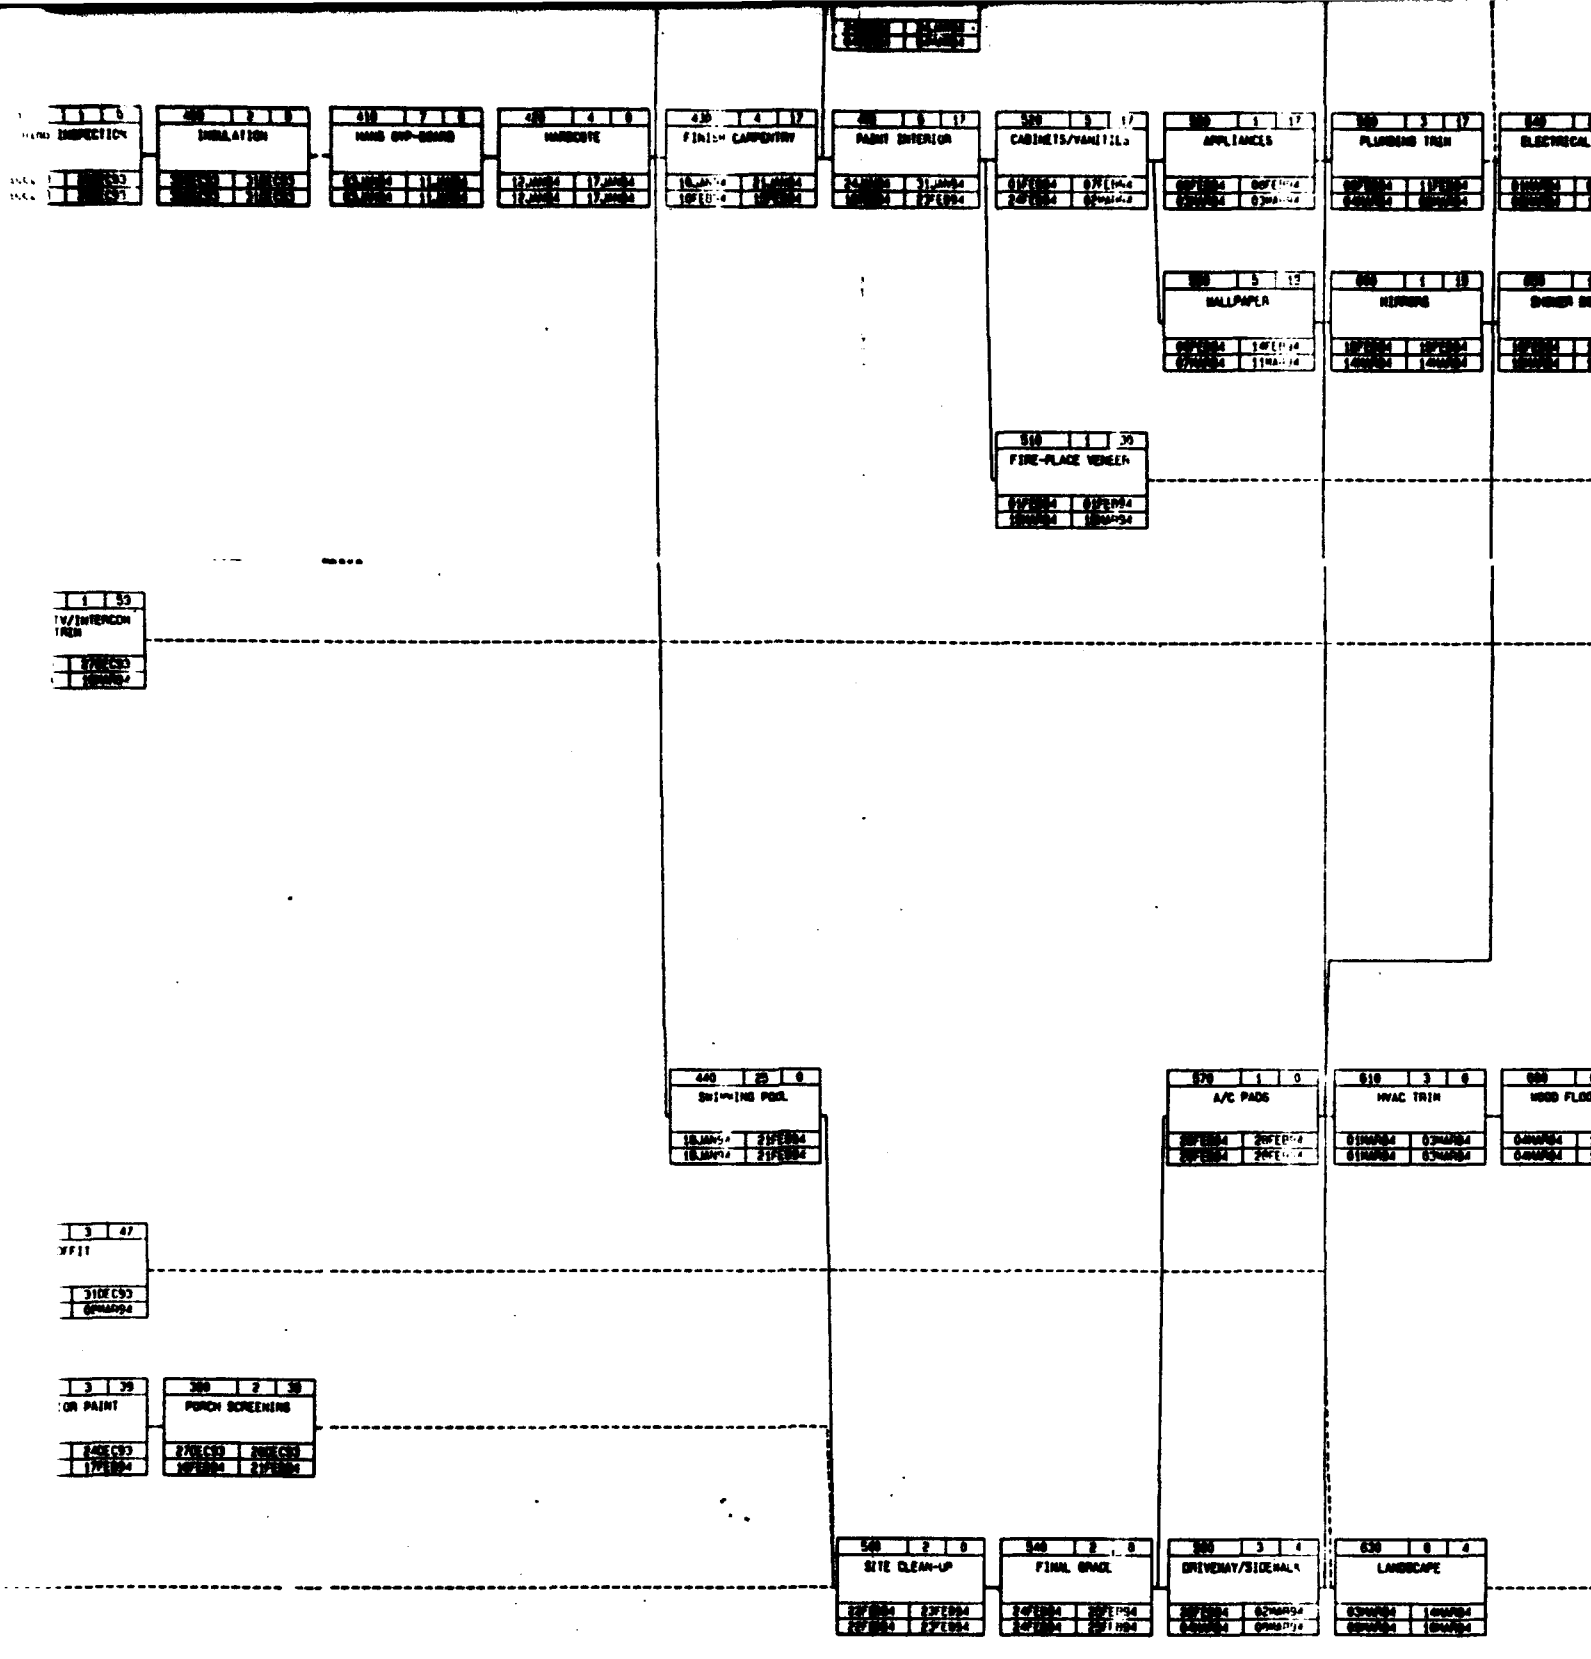


Plot Date: 10/1/84
 Data Date: 10/1/84
 Project Start: 10/1/84
 Project Finish: 10/1/84
 © Professional Builders, Inc.

LEGEND

□ Task
 □ Dependency
 □ Milestone

TYPICAL HOUSE CPM
 PROFESSIONAL BUILDERS, INC.
 SAMPLE PURE LOGIC DIAGRAM

(a)

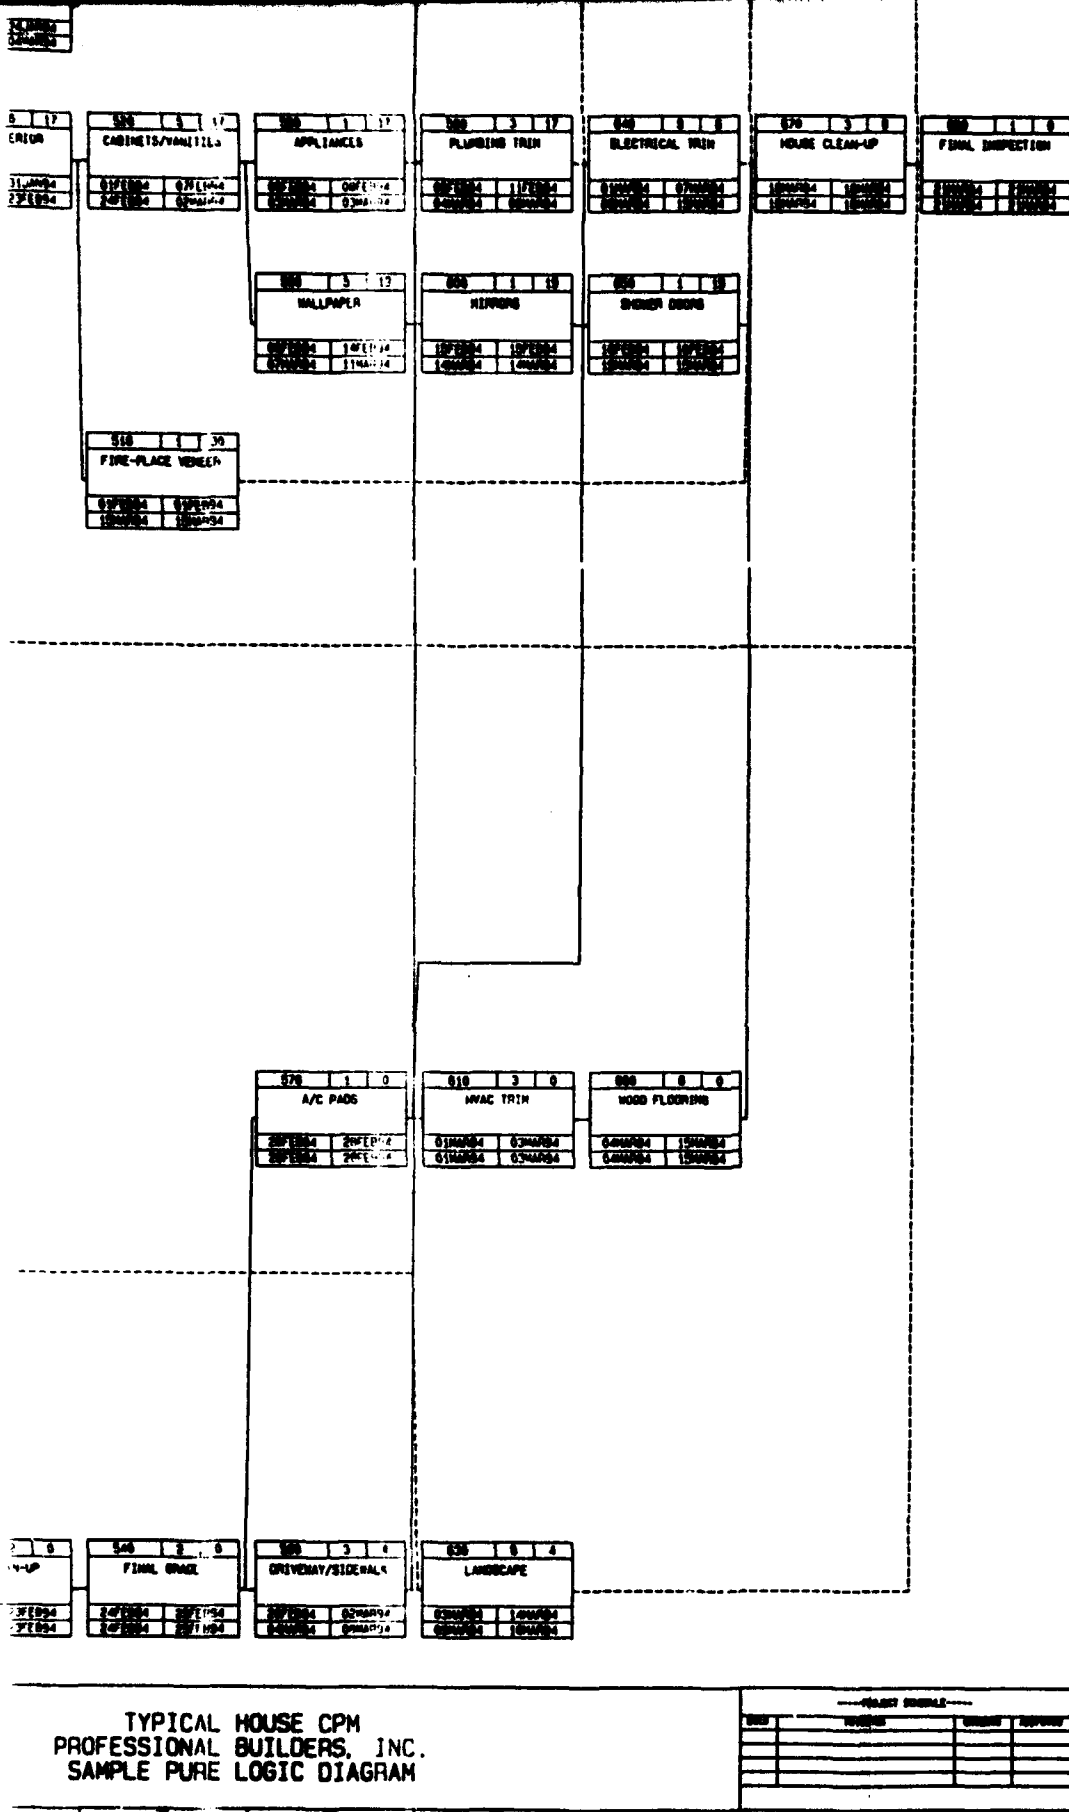

10
